










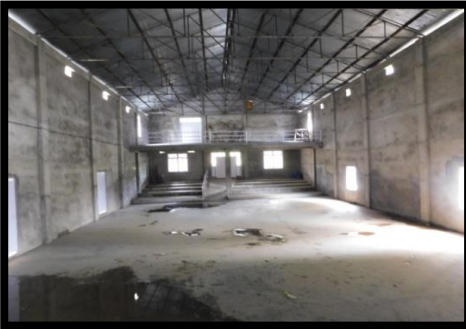

CONSTRUCTION OF KHLIEHMUSHUT AUDITORIUM CUM INDOOR GAMES COMPLEX, SHANGPUNG		
<div></div>		
Date of Inspection:	20.04.2018	
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G.Nongtdu, Executive Engineer and Shri L.L.Lyrwa, Junior Engineer	
Accompanied by:	Shri D. Shullet, Junior Engineer.	
Name of the Scheme:	Construction of Khliehmushut Auditorium Cum Indoor Games Complex, Shangpung	
Name of the MP:	Smt. Wansuk Syiem, MP(RS)	
Year recommended/sanctioned:	2017-18	
Amount & Date of sanctioned by the DC:	Rs. 25,00,000/- sanctioned on 15 th November 2014	
Reason for delay of sanction, if any:	Nil	
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 12,50,000/- released from Block Office on 20 th December 2017. -----	
Reason for delay in release of fund, if any:	Nil	
Amount utilized:	Rs. 12,50,000/-	
Date of commencement/starting of the work:	21 st December 2017	
Date of completion/Expected date of completion:	-----	
Status of the work:	Work is under progress	
Cause/Reason for delay in sanction/completion of works:	Nil	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.	
Name of executing agency:	The work is executed by the Local Committee of Shangpung Khliehmushut	
Whether signboard erected or not:	No	
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	Submitted to BDO, Laskein C&RD Block on 15 th March 2018. -----	
In case of completed Scheme whether the completion Report/ Certificate submitted to BDO/DC:	-----	
Impact of the scheme:	Benefitted the local people for their various needs like public awareness programmes, Dorbar meetings, award ceremonies, indoor sports, concerts , etc.	
Findings/Observations:	<ol style="list-style-type: none">1. Inspection was carried out in the presence of the Headman and other members of the Village Committee.2. The inspection team found that the construction of the Auditorium cum Indoor Games Complex is under progress. The Headman, Shangpung Khliemushut informed that during the year 2008 the Plan and Estimate amounted to Rs. 1.40 Crore. He then informed that the building has been constructed through village funds and also from the donations of the people of the village.3. He also informed that Rs. 6 lakhs had been received from the MLA Scheme and Rs. 1, 50,000 from the MDC Scheme. The amount from both the schemes was utilised for construction of the building.4. It was observed that the interior painting, walling, flooring at basement, is yet to be started.5. The quality and progress of work is very satisfactory.6. The Headman, Shangpung Khliemushut was advised to erect a signboard with complete details of the scheme after the completion of the building.7. Its dimension:- Column size: (35*35) cm. Tie beam: (30*30) cm. Floor Beams : (30*25) cm	

CONSTRUCTION OF RCC BUILDING OF LUMRANGNAH GOVT. L.P. SCHOOL, SHANGPUNG		
<div></div> <div></div>		
Date of Inspection:	20.04.2018	
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G.Nongtdu, Executive Engineer and Shri L.L.Ljyrwa, Junior Engineer	
Accompanied by:	Shri D. Shullet, Junior Engineer.	
Name of the Scheme:	Construction of RCC Building of Lumrangnah Govt. L.P. School, Shangpung	
Name of the MP:	Smt. Wansuk Syiem, MP(RS)	
Year recommended/sanctioned:	2017-18	
Amount & Date of sanctioned by the DC:	Rs 25,00,000/- sanctioned on 15 th November 2017.	
Reason for delay in sanction, if any:	Nil	
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 12,50,000/- released from Block Office on 20 th December 2017. -----	
Reason for delay in release of fund, if any:	Nil	
Amount utilized:	Rs. 12,50,000/-	
Date of commencement/starting of the work:	21 st December 2017.	
Date of completion/Expected date of completion:	-----	
Status of the work:	Work is under progress	
Cause/Reason for delay in sanction/completion of works:	Nil	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.	
Name of executing agency:	The work is executed by the School Managing Committee, Lumrangnah Govt. L.P. School, Shangpung	
Whether signboard erected or not:	No	
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	Submitted to BDO, Laskein C&RD Block on 17 th April 2018. -----	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	-----	
Impact of the scheme:	It is a positive impact to the students and the community as it will benefit them for achieving higher academic standards, motivation and achievements. Moreover it will remove congestion of students as additional classrooms are being added which will eventually lead to upgradation of the school in future.	
Findings/Observations:	<div>1. During inspection the team found that the construction of the school building is under progress. It is a three storey building.</div> <div>2. It has been seen that the structural works, walling, windows fitting, chowkat, plastering walling & ceiling, are completed and the remaining works are doors fitting, windows glass panes fixing, Veranda railing, and walling, plastering, doors & windows fitting, glass panes at top floor.</div> <div>3. It was informed by the School Managing Committee that the people of the village contributed towards the construction of the school building in the form of community work during laying of slab, etc.</div> <div>4. Its dimension:-<div>Plinth Area: L=4.10m and B=8m.</div><div>Column Size: (45*38) cm.</div><div>Beam: (30*30) cm.</div><div>Slab: Length =15m, Breadth =9m and thickness=100mm.</div></div> <div>5. The School Managing Committee has been advised to erect a signboard with complete details after completion of the Scheme.</div>	

CONSTRUCTION OF PLAYGROUND AT BIAR VILLAGE, WEST JAINTIA HILLS DISTRICT			
			
Date of Inspection:		20.04.2018	
Team of inspection officers:		Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G.Nongtdo, Executive Engineer and Shri L.L.Lyrwa, Junior Engineer	
Accompanied by:		Shri P. Wann, Gram Sevak and Shri D. Shullet, Junior Engineer.	
Name of the Scheme:		Construction of Playground at Biar Village, West Jaintia Hills District	
Name of the MP:		Smt. Wansuk Syiem, MP(RS)	
Year recommended/sanctioned:		2017-18	
Amount & Date of sanctioned by the DC:		Rs. 25,00,000/- sanctioned on 8 th December 2017.	
Reason for delay in sanction, if any:		Nil	
Date of release of fund:			
1 st instalment :-		Rs. 12,50,000/- released from Block Office on 17 th April 2018.	
2 nd instalment :-		-----	
Reason for delay in release of fund, if any:		Nil	
Amount utilized:		Rs. 12,50,000/-	
Date of commencement/starting of the work:		18 th April 2018.	
Date of completion/Expected date of completion:		-----	
Status of the work:		Work is under progress	
Cause/Reason for delay in sanction/completion of works:		Nil	
Whether inspection carried out from Block/DCs office:		Yes, at regular intervals from Block Office.	
Name of executing agency:		The work is executed by the Village Local Committee	
Whether signboard erected or not:		No	
Date of submission of UC:			
1 st Instalment:		-----	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:		-----	
Impact of the scheme:	Benefits the Biar Village for their various needs such as awareness programmes , Public meeting, tournaments , competition .etc.		
Findings/Observations:	<div>1. The inspection team found that the construction of playground is under progress.</div> <div>2. It was observed that earthwork cutting and filling is completed and Goal posts have been erected and the remaining work is kutch side drains.</div> <div>3. It was informed by the Village Committee that after signing the agreement with the Deputy Commissioner the work has been started first by the village funds while awaiting the 1st and 2nd instalment. They then informed that the earth cutting of the playground was done by JCB machine and the dressing was done by the villagers.</div> <div>4. It was found that the quality of construction of the Playground was very good and it appears that the fund was rightly used for the purpose.</div> <div>5. The Village committee has been advised to erect a signboard in complete details after completion of the scheme.</div> <div>6. Its dimension:<div>Length=95m and Breadth=80m.</div><div>Goal Post = 150mm diameter</div></div>		

CONSTRUCTION OF DISPENSARY BUILDING AT SAHSNIANG SACRED HEART HEALTH CENTER			
<div></div>			
Date of Inspection:		20.04.2018	
Team of inspection officers:		Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G.Nongtdu, Executive Engineer and Shri L.L.Ljyrwa, Junior Engineer	
Accompanied by:		Shri S.M. Chyrmang, Gram Sevak, Shri M. Suchiang, Gram Sevak and Shri D. Shullet, Junior Engineer.	
Name of the Scheme:		Construction of Dispensary building at Sahnsniang Sacred Heart Health Center	
Name of the MP:		Shri V.H Pala, MP(LS)	
Year recommended/sanctioned:		2017-18	
Amount & Date of sanctioned by the DC:		Rs. 10,00,000/- sanctioned on 9 th November 2017	
Reason for delay in sanction, if any:		Nil	
Date of release of fund: 1 st instalment :- 2 nd instalment :-		Rs. 5,00,000/- released from Block Office on 28 th November 2017. -----	
Reason for delay in release of fund, if any:		Nil	
Amount utilized:		Rs. 5,00,000/-	
Date of commencement/starting of the work:		29 th November 2017.	
Date of completion/Expected date of completion:		-----	
Status of the work:		Work is under progress	
Cause/Reason for delay in sanction/completion of works:		Nil	
Whether inspection carried out from Block/DCs office:		Yes, at regular intervals from Block Office.	
Name of executing agency:		The work is executed by the Local Committee Sahnsniang Sacred Heart Health Center	
Whether signboard erected or not:		No	
Date of submission of UC: 1 st Instalment: 2 nd Instalment:		Submitted to the BDO, Laskein C&RD Block on 4 th December 2017. -----	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:		-----	
Impact of the Scheme:		The presence of the Dispensary at Sahnsniang has benefitted the people of the area.	
Findings/Observations:		<div>1. On inspection the team observed that the construction of dispensary building is completed. It is constructed with good quality materials workmanship.</div> <div>2. The Committee informed the team that they have spent from their own funds for completion of the building while awaiting the 2nd instalment.</div> <div>3. The building consists of 3 rooms whereby Room No 1 is the patient's room with 3 beds with attached bathroom, Room No 2 is the Pharmacy Room and Room No 3 is the Emergency Room.</div> <div>4. It was informed by the Committee that voluntary work has been done by the people from the village to help in construction of the dispensary.</div> <div>5. The Committee has been advised to erect a signboard with complete details of the scheme.</div> <div>6. Its dimension:<div>Plinth Area: L=77m and B=75m.</div><div>Column size: (32*28) cm-----Beam=32*28cm.</div><div>Chowkat1: (12*6*480) cm-----Chowkat2: (12*6*450) cm.</div><div>Door1: 90*190cm (2 nos) -----Door2: 65*195 (2nos).</div><div>Toilet/Bathroom: Length =180cm and Breadth=210cm.</div><div>Flush door: (75*150) cm.</div><div>Window1: (1.20*1.80) m (2nos) -----Window2: (1.80*1.80)m (2nos).</div><div>Pharmacy Room: Length=230 cm and Breadth =200cm.</div></div>	

CONSTRUCTION OF GALLERY AT BIAR NOHRONG OF THADMUTHLONG		
<div></div>		
Date of Inspection:	20.04.2018	
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G.Nongtdu, Executive Engineer and Shri L.L.LJyrwa, Junior Engineer	
Accompanied by:	Shri M.Suiam, Gram Sevak and Shri D. Shullet, Junior Engineer.	
Name of the Scheme:	Construction of Gallery at Biar Nohrong of Thadmuthlong	
Name of the MP:	Shri V.H Pala, MP(LS)	
Year recommended/sanctioned:	2017-18	
Amount & Date of sanctioned by the DC:	Rs. 15,00,000/- sanctioned on 4 th December 2017.	
Reason for delay in sanction, if any:	Nil	
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 9,00,000/- released from Block Office on 19 th December 2017. -----	
Reason for delay in release of fund, if any:	Nil	
Amount utilized:	Rs. 9,00,000/-	
Date of commencement/starting of the work:	18 th December 2017	
Date of completion/Expected date of completion:	-----	
Status of the work:	Work is under progress	
Cause/Reason for delay in sanction/completion of works:	Nil	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.	
Name of executing agency:	The work is executed by the Local Committee Sein Raji Muthlong, Thadmuthlong	
Whether signboard erected or not:	No	
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	-----	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	-----	
Impact of the Scheme:	Benefit for the people for holding their Cultural events.	
Findings/Observations:	<div>1. During inspection the team found that the construction of gallery is under progress.</div> <div>2. It also been observed that the earth work excavation has been completed.</div> <div>3. The committee has been advised to erect a signboard with complete details after completion of the scheme</div> <div>4. Its dimension: Length=48m and B=73m.</div>	
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-	
Shri S.Sungoh, Research Officer Programme Implementation & Evaluation	-	
Shri R.M.G.Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-	
Shri L.L.L. Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-	
