

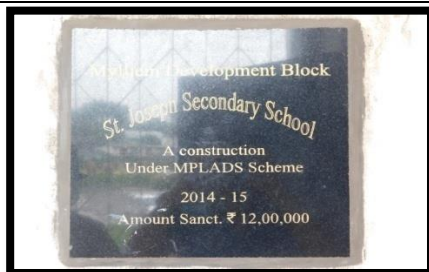


CONSTRUCTION OF SCHOOL BUILDING OF ST. JOSEPH SEC. SCHOOL, LAITKOR

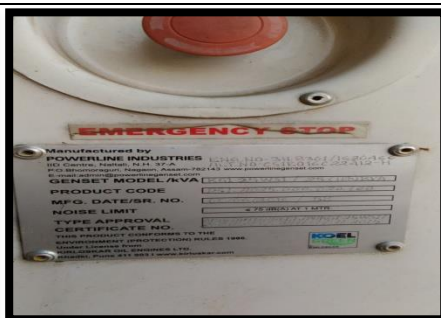

Date of Inspection:	11 th August 2017	
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block	
Name of the Scheme:	Construction of School Building of St. Joseph Sec. School, Laitkor	
Name of the MP:	Smt. W. Syiem, MP(RS)	
Year recommended/sanctioned:	2014-15	
Amount & Date of sanction by the DC:	Rs. 12,00,000/- sanctioned on 2 nd July 2015	
Reason for delay of sanction, if any:	Nil	
Date of release of fund:		
1 st instalment :-	11 th August 2015	
2 nd instalment :-	23 rd March 2016	
Reason for delay in release of fund, if	Nil	
Amount utilized:	Rs. 12,00,000/-	
Date of commencement/starting of the work:	10 th August 2015	
Date of completion/Expected date of completion:	20 th March 2016	
Status of the work:	Work completed	
Cause/Reason for delay in sanction/completion of works:	Nil	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.	
Name of executing agency:	The work is executed by the Managing Committee of the School	
Whether signboard erected or not:	Yes	
Date of submission of UC:		
1 st Instalment:	-----	
2 nd Instalment:		
In case of completed Scheme whether the completion Report/ Certificate submitted to BDO/DC:	Yes	
Impact of the scheme:	Positive impact on the students and community, setting higher academic standards, teacher motivation and higher student achievements.	
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of school building is completed. It was constructed with good quality materials and good workmanship. It consists of 3 rooms. Its dimension: <ul style="list-style-type: none"> Plinth area: L=12.4 and B=6m-----Room1: L=7.8m and B=6m. Window1: H=1.5m and B=1.2m (3nos)-----Door1: H=1.9m and B=78cm. Chowkat: (12*6*540)cm-----Room2: L=7.8m and B=5.8m. Door2: H=1.9m and B=78cm (2nos)-----Window2: H=1.5m and B=1.2m (6nos). Veranda: L=12.4 and B=2m-----Veranda Railing & Grill: L=12.4m and H=1.50m. Veranda Brick Railing: L=12.4m and H=0.80m.-----Stair: L=4.5m, Riser=30cm and Tread=12cm.-----Stair Railing: L=4.2m and H=0.70m. The JE was advised to inform the School Managing Committee to make a correction on the plaque mentioning the name of MP, date of commencement & completion ,etc. 	

PROVIDING OF DG SET FOR ST. JOSEPH SEC. SCHOOL, LAITKOR INCLUDING FABRICATION ETC.

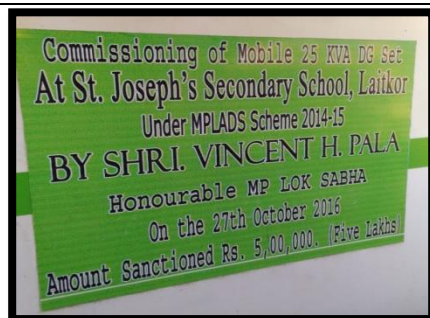


Date of Inspection:	11 th August 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block
Name of the Scheme:	Providing of DG Set for St. Joseph Sec. School, Laitkor Including Fabrication etc.
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2015-16
Amount & Date of sanction by the DC:	Rs 5,00,000/- sanctioned on 27 th October 2015
Reason for delay in sanction, if any:	Nil
Date of release of fund:	
1 st instalment :-	16 th February 2016.
2 nd instalment :-	29 th September 2016.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	17 th February 2016
Date of completion/Expected date of completion:	15 th October 2017
Status of the work:	95% Work Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Managing Committee of the School.
Whether signboard erected or not:	Yes, on the body of the Genset.
Date of submission of UC:	
1 st Instalment:	-----
2 nd Instalment:	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	-----
Impact of the scheme:	Benefit for the School as an auxiliary unit in case of power shortages.
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team was informed that the DG set is not yet installed in the school since additional work has to be done on the chassis so that it can be towed. The JE was advised to inform the School Managing Committee to complete the pending work so as to facilitate installation of the Genset.

EXTENSION OF MADANRTING PRESBYTERIAN SECONDARY SCHOOL




Date of Inspection:	11 th August 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block
Name of the Scheme:	Extension of Madanrtng Presbyterian Sec. School
Name of the MP:	Smt. W. Syiem, MP(RS)
Year recommended/sanctioned:	2013-14
Amount & Date of sanction by the DC:	Rs. 9,17,000/- sanctioned on 3 rd December 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	20 th January 2015 2 nd March 2016
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 9,17,000/-
Date of commencement/starting of the work:	25 th January 2015
Date of completion/Expected date of completion:	30 th February 2016
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Managing Committee
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	----- -----
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Additional infrastructure so that additional rooms can accommodate the students.
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the extension of school building was completed. The school building was constructed with good quality materials and good workmanship. It consists of two class rooms. Its dimension: Plinth area: L=22m and B=5m Room1: L=7m and B=6m---Windows: H=1.8m and B=1.6m (16 nos) Door: H=1.9m and B=1.8m (5nos) -----Chowkat:((7*10*490) cm. Room2: L=7m and B=6m---Windows: H=1.8m and B=1.6m (16 nos) Door: H=1.9m and B=1.8m (5nos) -----Chowkat:(7*10*490) cm. Parapet: L=22m and H=1m----- Veranda: L=22m and B=1m. The School Managing Committee was advised to erect a plaque mentioning complete details of the scheme.

SOLAR STREET LIGHTS AT MADANRTING TO COVER DIFFERENT LOCALITIES

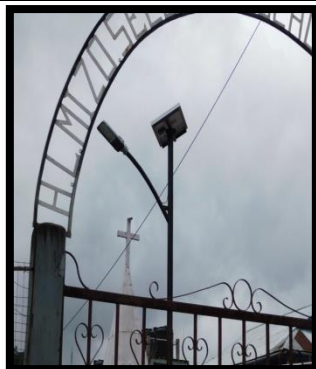

Date of Inspection:	11 th August 2017	
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block	
Name of the Scheme:	Solar Street Lights at Madanrting to Cover different localities	
Name of the MP:	Smt. W. Syiem, MP(RS)	
Year recommended/sanctioned:	2016-17	
Amount & Date of sanction by the DC:	Rs.50,00,000/- sanctioned	
Reason for delay in sanction, if any:	Nil	
Date of release of fund:	14 th September 2016 -----	
1st instalment :-		
2nd instalment :-		
Reason for delay in release of fund, if any:	Nil	
Amount utilized:	Rs. 45,00,000/-	
Date of commencement/starting of the work:	14 th September 2016	
Date of completion/Expected date of completion:	-----	
Status of the work:	95% Work completed	
Cause/Reason for delay in sanction/completion of works:	Nil	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.	
Name of executing agency:	The work is executed by the Local Committee.	
Whether signboard erected or not:	No	
Date of submission of UC:	-----	
1st instalment :-		
2nd instalment :-		
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes	
Impact of the Scheme:	A safety measure for the inhabitants in case of power shortages and benefit for the localities within Madanrting where there are no streetlights.	
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the installation of Solar lights at Madanrting was completed. The inspection team was informed by the members of the Dorbar Shnong of Madanrting that there are 70 nos of Solar lights covering almost all the localities under Madanrting. It was found that there are 3 (three) types of solar lights used depending upon the requirement and location of the sites. There are 18, 24 & 30 watts LED bulbs along with normal batteries except for 30 watts lights where lithium-ion batteries were used. The Dorbar Shnong was advised to erect a plaque mentioning complete details of the scheme at a central location. 	

CONSTRUCTION OF FOOTPATH AT NONGRAH, EAST KHASI HILLS DISTRICT

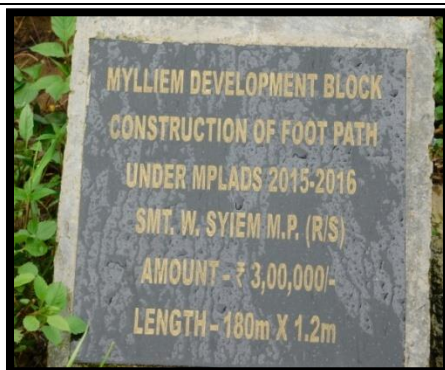


Date of Inspection:	11 th August 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdo, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block
Name of the Scheme:	Construction of Footpath at Nongrah, East Khasi Hills District
Name of the MP:	Smt. W. Syiem, MP(RS)
Year recommended/sanctioned:	2016-17
Amount & Date of sanction by the DC:	Rs. 3,00,000/-
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1st instalment :- 2nd instalment :-	12 th October 2016. 30 th May 2017.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 3,00,000/-
Date of commencement/starting of the work:	1 st August 2016
Date of completion/Expected date of completion:	30 th November 2016
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Local Committee.
Whether signboard erected or not:	Yes
Date of submission of UC: 1st instalment :- 2nd instalment :-	-----
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	A permanent means to provide access to the inhabitants of the localities.
Findings/Observations:	<ol style="list-style-type: none"> During inspection it has been seen that the construction of footpath is completed. It was constructed with good quality materials. Its dimension: Length=180m and Width=1.2m

PROVIDING ASSISTANCE FOR CONSTRUCTION OF FOOTPATH AT DORBAR DONG RYNG RYNJAH



Date of Inspection:	11 th August 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdo, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block
Name of the Scheme:	Providing Assistance for Construction of Footpath at Dorbar Dong Rynjah
Name of the MP:	Smt. W. Syiem, MP (RS).
Year recommended/sanctioned:	2015-16
Amount & Date of sanction by the DC:	Rs. 3,00,000/- sanctioned on 27 th November 2015
Reason for delay in sanction, if any:	Nil
Date of release of fund:	
1 st instalment :-	19 th January 2016.
2 nd instalment :-	13 th April 2016.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 3,00,000/-
Date of commencement/starting of the work:	1 st June 2016
Date of completion/Expected date of completion:	29 th March 2016
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Local Committee Dorbar Dong Rynjah
Whether signboard erected or not:	Yes
Date of submission of UC:	
1 st Instalment:	-----
2 nd Instalment:	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	A permanent means to provide access to the inhabitants of the localities.
Findings/Observations:	<ol style="list-style-type: none"> 1. The construction of the footpath is completed. 2. Its dimension: L=104m and B=3.5m. 3. The member of the Dorbar Shnong was advised to make a correction on a plaque mentioning the name of MP. 4. The quality of work is satisfactory.

CONSTRUCTION OF MAIN DRAIN AT UMPLING DONGSHANENG, UMPLING

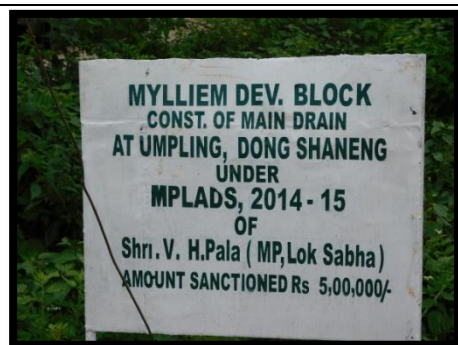

Date of Inspection:	11 th August 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block
Name of the Scheme:	Construction of Main Drain at Umpling Dongshaneng, Umpling
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanction by the DC:	Rs. 5,00,000/- sanctioned on 22 nd December 2015
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	18 th October 2016. -----
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 2,50,000/-
Date of commencement/starting of the work:	20 th October 2016
Date of completion/Expected date of completion:	15 th September 2017
Status of the work:	Work completed & final payment will be released soon, waiting for 2 nd instalment.
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Local Committee
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	-----
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Additional benefit for the locality since drain is covered and can be used as a footpath which can be accessed by the inhabitants of the locality.
Findings/Observations:	<ol style="list-style-type: none"> On inspection it was found that the construction of Main Drain is completed. It was also observed that additional work that has been done is C.C footpath on top of the drain. Its dimension: Footpath: Length=63m and width=2.6m. Main drain: Length=63m, width=1.2m and Slab Thickness: 12mm. The JE was advised to inform the Committee to submit UC's and photograph for release of 2nd instalment. The quality of work is satisfactory.

CONSTRUCTION OF FOOTPATH, WASHING PLATFORM AT WAHRTING, MADANRTING




Date of Inspection:	11 th August 2017	
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block	
Name of the Scheme:	Construction of Footpath, washing platform at Wahrting, Madanrting	
Name of the MP:	Smt. W. Syiem, MP (RS).	
Year recommended/sanctioned:	2014-15	
Amount & Date of sanction by the DC:	Rs. 5,22,000/- sanctioned on 14 th July 2015	
Reason for delay in sanction, if any:	Nil	
Date of release of fund:		
1 st instalment :-	7 th January 2016.	
2 nd instalment :-	30 th July 2016.	
Reason for delay in release of fund, if any:	Nil	
Amount utilized:	Rs. 5,22,000/-	
Date of commencement/starting of the work:	5 th January 2016	
Date of completion/Expected date of completion:	30 th July 2016	
Status of the work:	Completed	
Cause/Reason for delay in sanction/completion of works:	Nil	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.	
Name of executing agency:	The work is executed by the Local Committee	
Whether signboard erected or not:	No	
Date of submission of UC:		
1 st Instalment:	-----	
2 nd Instalment:		
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes	
Impact of the Scheme:	Benefit for the locality as footpath makes it accessible for the people of the locality to have access to the water & washerwomen have a place to wash their clothes.	
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of footpath and washing platform covered with CGI sheet was completed. It was constructed with good quality materials and workmanship. Its dimension: Washing shed and platform L=11.3m, B=3.4m and H=3m-----Plinth Height: 90cm. Column size (12 nos):(20*20)cm Footpath: L=87m and B=1.7m. The Dorbar Shnong was advised to erect a plaque with complete details of the scheme mentioning name of MP, amount sanctioned, date of starting & completion ,etc. 	

CONSTRUCTION OF SCHOOL BUILDING OF H.L. MIZO SEC. SCHOOL, HAPPY VALLEY, SHILLONG



Date of Inspection:	11 th August 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block
Name of the Scheme:	Construction of School Building of H.L.Mizo Sec. School, Happy Valley, Shillong
Name of the MP:	Smt. W. Syiem, MP (RS).
Year recommended/sanctioned:	2013-14
Amount & Date of sanction by the DC:	Rs. 10,00,000/- sanctioned on 11 th June 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	2 nd September 2014. 29 th July 2015.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 10,00,000/-
Date of commencement/starting of the work:	2 nd September 2015
Date of completion/Expected date of completion:	24 th July 2015
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Managing Committee of the School.
Whether signboard erected or not:	Yes
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	-----
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Positive impact on the students and community, setting higher academic standards, teacher motivation and higher student achievements.
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of school building is completed. Its consists of two class rooms, one room is at Ground Floor and other room is at First Floor Its dimension: Plinth Area: Ground floor: L=8m and B=7m-----First floor: L=8m and B=7m. Door: Height=1.2m Breadth =90m (2nos) Windows: Height=1.2m and Breadth =0.9m (4nos) Parapets: Length=15m and Height=0.90m Staircase: Length=4.2m, Riser= 32cm and Tread=15cm. GI Pipe Railing: 25mm Column size: 25*25 cm Beam size: 25*25 cm.

CONSTRUCTION OF SCIENCE LABORATORY ROOM FOR H.L. MIZO SEC. SCHOOL, SHILLONG

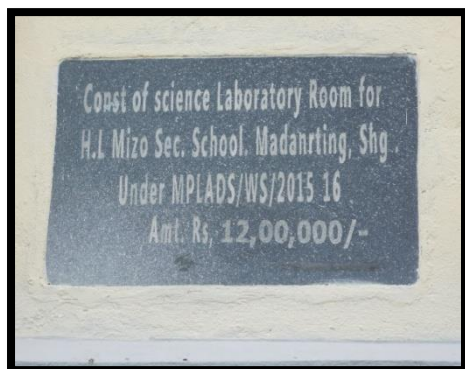


Date of Inspection:	11 th August 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block
Name of the Scheme:	Construction of Science Laboratory Room for H.L.Mizo Sec. School, Happy Valley, Shillong
Name of the MP:	Smt. W. Syiem, MP (RS).
Year recommended/sanctioned:	2015-16
Amount & Date of sanction by the DC:	Rs. 12,00,000/- sanctioned on 11 th June 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund:	
1 st instalment :-	13 th January 2016.
2 nd instalment :-	23 rd August 2016.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 12,00,000/-
Date of commencement/starting of the work:	01/12/2015
Date of completion/Expected date of completion:	30/07/2015
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Managing Committee of the School.
Whether signboard erected or not:	Yes
Date of submission of UC:	
1 st Instalment:	-----
2 nd Instalment:	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Additional benefit for the students of the school towards a better mode of learning.
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of laboratory is completed. Its consists of two rooms i.e. science lab and class room. Its dimension: Ground floor: L=7.5m and B=7m. -----First Floor: L=7.5m and B=7m. Door: H=1.2m and B=90m (2nos)-----Windows: H=1.2m and B=0.9m (4nos) Chowkat: (7*10*420) cm. Column size: (25*25) Cm Beam size: (25*25) cm.

CONSTRUCTION OF FENCING WALL AT CEMETERY (LUMJINGTEP SHNONG), MADANRTING



Date of Inspection:	11 th August 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block
Name of the Scheme:	Construction of Fencing Wall at Cemetery (Lumjingtep Shnong), Madanrting
Name of the MP:	Smt. W. Syiem, MP (RS).
Year recommended/sanctioned:	2014-15
Amount & Date of sanction by the DC:	Rs. 14,24,300/- sanctioned on 14 th July 2015
Reason for delay in sanction, if any:	Nil
Date of release of fund:	
1 st instalment :-	7 th January 2016.
2 nd instalment :-	28 th September 2016.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 14,24,300/-
Date of commencement/starting of the work:	7 th January 2016
Date of completion/Expected date of completion:	23 rd September 2016
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Local Committee
Whether signboard erected or not:	Yes
Date of submission of UC:	
1 st Instalment:	-----
2 nd Instalment:	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Demarcation of boundary and to prevent encroachment of miscreants.
Findings/Observations:	<ol style="list-style-type: none"> During Inspection, it has been seen that the construction of fencing was completed. Its dimension: Gate: Length=3.6m and Height=1.8m Column size: (35* 35) cm and H=2.50m. The Dorbar Shnong has been advised to erect a plaque with full complete details of the scheme such as mentioning the name of MP, amount sanction, date of starting & completion .etc

CONSTRUCTION OF SCHOOL BUILDING OF ST. PETER'S SECONDARY SCHOOL, MADANRTING

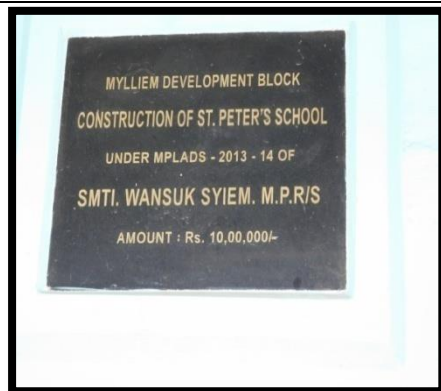

Date of Inspection:	11 th August 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block
Name of the Scheme:	Construction of School Building of St. Peter's Sec. School, Madanrting
Name of the MP:	Smt. W. Syiem, MP (RS).
Year recommended/sanctioned:	2013-14
Amount & Date of sanction by the DC:	Rs. 10,00,000/- sanctioned on 30 th June 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund:	
1 st instalment :-	2 nd September 2014.
2 nd instalment :-	29 th July 2015.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 10,00,000/-
Date of commencement/starting of the work:	3 rd September 2014
Date of completion/Expected date of completion:	20 th July 2015
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Managing Committee
Whether signboard erected or not:	Yes
Date of submission of UC:	
1 st Instalment:	-----
2 nd Instalment:	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Positive impact on the students and community, setting higher academic standards, teacher motivation and higher student achievements.
Findings/Observations:	<ol style="list-style-type: none"> On inspection it has been observed that the construction of school was completed. It was constructed with good quality materials. The school building consists of 3 storeys. It was informed that ₹12 lakhs (approx) has been contributed from the School Managing Committee and also help in the form of community participation from the locality. Its dimension: Plinth area: L=18m and B=8m----(windows 9 nos)150cm * 150cm Door: 90cm * 190cm (3 nos of door) Chowkat: (10*6*420) cm.

EXTENSION OF COMMUNITY HALL AT NONGKHYRIEM, NONGTHYMMAI



Date of Inspection:	11 th August 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block
Name of the Scheme:	Extension of Community Hall at Nongkhyriem, Nongthymmai
Name of the MP:	Shri V.H. Pala, MP(LS)
Year recommended/sanctioned:	2015-16
Amount & Date of sanction by the DC:	Rs. 5,00,000/- sanctioned on 10 th December 2015
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	1 st March 2016 -----
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 2,50,000/-
Date of commencement/starting of the work:	2 nd March 2016
Date of completion/Expected date of completion:	-----
Status of the work:	40% Work in progress
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Local Committee
Whether signboard erected or not:	Not yet
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	----- -----
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	-----
Impact of the Scheme:	Benefit for locality for conducting programme such as Dorbar meeting, public awareness programmes, etc.
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the extension of community hall is under progress. It has been observe that Column footing, Column, Plinth beam are completed, where as shuttering works for floor beam and slab, steel reinforcement for slab is under progress. Its dimension: Plinth area: Length=6m and Breadth=3m----- Column size: (25*25)cm and Height =3.2m The Village Dorbar has been advised to erect a plaque with complete I details after completion of the scheme.

CONSTRUCTION OF COMMUNITY HALL FOR RNGI RUM, NONGTHYMMAI



Date of Inspection:	11 th August 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block
Name of the Scheme:	Construction of Community Hall for Rngi Rum, Nongthymmai
Name of the MP:	Shri V.H. Pala, MP(LS)
Year recommended/sanctioned:	2013-14
Amount & Date of sanction by the DC:	Rs. 5,00,000/- sanctioned on 9 th June 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund:	
1 st instalment :-	15 th January 2015
2 nd instalment :-	-----
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	16 th January 2015
Date of completion/Expected date of completion:	20 th March 2016
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Local Committee
Whether signboard erected or not:	Yes
Date of submission of UC:	
1 st Instalment:	-----
2 nd Instalment:	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Help the locality for arranging Dorbar meeting, public awareness programmes, etc.
Findings/Observations:	<ol style="list-style-type: none"> During inspection it has been observed that the construction of Community Hall is completed. It was constructed with good quality materials. It was informed by the members of the Local Committee that there was convergence of many schemes towards the construction of the Community Hall. Its dimension: Plinth area Length=9m and Breadth =6m-----Column size: (35*45) cm and H=3m. Tie beam: 90cm*30cm. Staircase: Length=6m, Thread=32cm and Riser=15cm----- Staircase Railing: Length =6m GI Pipes:40mm (6 nos). Door: 100cm *200cm Chowkat: (10*7 *510)cm Door1: 60*180cm (2nos). Window: 150cm*150cm (5 nos)----- Door2: 90cm*185cm. Verandah Grill: L=3.6m and H=1.6m-----Parapet: H=90cm and L=3.6m. Gate: Length =75cm and Height =240cm The quality of work is satisfactory.

CONSTRUCTION OF FENCING LUMJINGTHANG, LAWJYNRIEW



Date of Inspection:	11 th August 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri B. Wanniang, Junior Engineer, Myllem Block
Name of the Scheme:	Construction of Fencing Lumjingthang, Lawjynriew
Name of the MP:	Smt. W. Syiem, MP (RS).
Year recommended/sanctioned:	2015-16
Amount & Date of sanction by the DC:	Rs. 4,00,000/- sanctioned on 24 th November 2015
Reason for delay in sanction, if any:	Nil
Date of release of fund:	
1 st instalment :-	4 th January 2017.
2 nd instalment :-	-----
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 2,00,000/-
Date of commencement/starting of the work:	4 th January 2017
Date of completion/Expected date of completion:	-----
Status of the work:	100% Work Completed demanding for 2 nd instalment from DC's Office
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Executive Committee, Seng Khasi Nongthymmai, Shillong
Whether signboard erected or not:	Yes
Date of submission of UC:	
1 st Instalment:	-----
2 nd Instalment:	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Boundary demarcation and to prevent encroachment of miscreants.
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of fencing is completed The Secretary has been advised to erect a plaque with complete details of the scheme. Its Dimension: Length = 60m Height=1.98m (average).
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G. Nongtdu, Executive Engineer Project Monitoring Unit under PI & Evaluation	-
Shri L.L.L. Jyrwa, Junior Engineer Project Monitoring Unit under PI & Evaluation	-
