



| CONSTRUCTION OF SCHOOL HOSTEL AT ST. FRANCIS DE SALES SECONDARY SCHOOL, MAWRYNGKNENG | | |
|---|---|---|
|  | | |
| Date of Inspection: | 15.07.2016 | |
| Team of inspection officers: | Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer | |
| Accompanied by: | Shri B. Nongsiej, Assistant Engineer | |
| Name of the Scheme: | Construction of School Hostel at St. Francis De Sales Secondary School, Mawryngkneng | |
| Name of the MP: | Shri V.H. Pala MP(LS) | |
| Year recommended/sanctioned: | 2013-14 | |
| Amount & Date of sanctioned by the | Rs. 5,00,000/- Sanctioned on 01 st December 2014 | |
| Reason for delay of sanction, if any: | Nil | |
| Date of release of fund: | Rs. 2,50,000/- released from Block Office on 02 nd February 2015. | |
| 1 st instalment :- | | |
| 2 nd instalment :- | ----- | |
| Reason for delay in release of fund, | Nil | |
| Amount utilized: | Rs. 2,50,000/- | |
| Date of commencement/starting of the work: | 15 th February 2015 | |
| Date of completion/Expected date of completion: | 31 st July 2016 | |
| Status of the work: | In progress (70% completed). | |
| Cause/Reason for delay in sanction/completion of works: | <p>(a) After the release of work order on the 15-02-2015, the School Managing Committee of the school verbally informed that the project they needed was additional classroom instead of hostel upon which the office of the BDO, Mawryngkneng advised him to submit application of the same for recast.</p> <p>(b) After delay of several months and show cause issued by the Office, the School Managing Committee verbally informed the office that they will start the project as per plan after the end of monsoon (October 2015).</p> | |
| Whether inspection carried out from Block/DCs office: | Yes, at regular intervals from Block Office. | |
| Name of executing agency: | The School Managing Committee, St. Francis De Sales Secondary School, Mawryngkneng. | |
| Whether signboard erected or not: | No | |
| Date of submission of UC: | Not yet received from beneficiary. | |
| 1 st Instalment: | | |
| 2 nd Instalment: | ----- | |
| In case of completed Scheme whether the completion Report/ Certificate submitted to BDO/DC: | Yes | |
| Impact of the scheme: | The Hostel will help in the overall development of the school. | |
| Findings/Observations: | <ol style="list-style-type: none"> 1. The inspection team found that the construction of school hostel is under progress, it is constructed on the top floor of the existing school building. 2. Column, Brick walling, door chowkat is completed, whereas, exterior and interior plastering, roof truss, CGI roof is yet to be started. 3. Its dimension, Plinth area, L=18.5m and B=9.3m, Door Chowkat (4 Nos), L=5.02m , H=10m and Thickness = 6m, Column size= 32cmx30cm. 4. The School Managing Committee was advised to erect a plaque with complete detail after completion of the scheme. | |
| Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation | | - |
| Shri S. Sungoh, Research Officer Programme Implementation & Evaluation | | - |
| Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | | - |
| Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | | - |

COMPUTERISATION OF DORBAR SHNONG MAWSHABUIT, MAWSHABUIT.

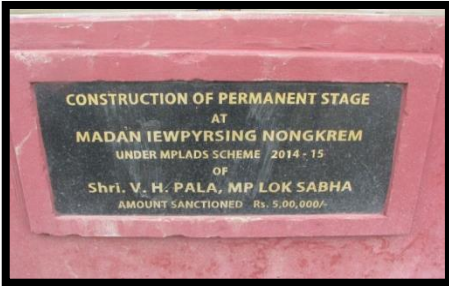




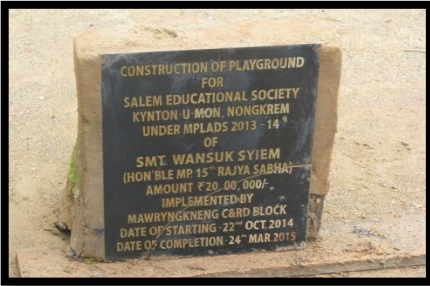


| | |
|--|--|
| Date of Inspection: | 15.07.2016 |
| Team of inspection officers: | Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer |
| Accompanied by: | Shri B. Nongsiej, Assistant Engineer. |
| Name of the Scheme: | Computerisation of Dorbar Shnong Mawshabuit, Mawshabuit. |
| Name of the MP: | Shri V.H. Pala MP(LS) |
| Year recommended/sanctioned: | 2013-14 |
| Amount & Date of sanctioned by the DC: | Rs 3,00,000/- sanctioned on 30 th January 2014 |
| Reason for delay in sanction, if any: | Nil |
| Date of release of fund: 1st instalment :- 2nd instalment :- | Rs. 1,50,000/- released from Block Office on 28 th February 2014. Rs. 1,50,000/- released from Block Office on 22 nd September 2014 |
| Reason for delay in release of fund, if any: | Nil |
| Amount utilized: | Rs. 3,00,000/- |
| Date of commencement/starting of the work: | 3 rd March 2014 |
| Date of completion/Expected date of completion: | 28 th August 2014 |
| Status of the work: | Completed |
| Cause/Reason for delay in sanction/completion of works: | |
| Whether inspection carried out from Block/DCs office: | Yes, at regular intervals from Block Office. |
| Name of executing agency: | Dorbar Shnong Mawshabuit, Mawshabuit. |
| Whether signboard erected or not: | No. (Temporary signboard was erected after completion of project) |
| Date of submission of UC: 1st Instalment: 2nd Instalment: | Submitted to BDO, Mawryngkneng C & RD Block on 11 th August 2014 Submitted to BDO, Mawryngkneng C & RD Block on 05 th June 2015 |
| In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC: | Yes |
| Impact of the scheme: | The computerization has helped the local Dorbar as well as the public in availing information of various developmental programmes of the Government. |
| Findings/Observations: | 1. On inspection it was found that there is 1 computer, 1 Xerox machine, 1 computer table, 1UPS, 1 battery, 1Chair and other equipments. 2. The members of the Dorbar were advised to erect the plaque with complete details. |
| Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation | - |
| Shri S. Sungoh, Research Officer Programme Implementation & Evaluation | - |
| Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI &Evaluation | - |
| Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI &Evaluation | - |

CONSTRUCTION OF ST. JOSEPH L.P SCHOOL, LAD KYNTON-U-MON, LAD NONGKREM

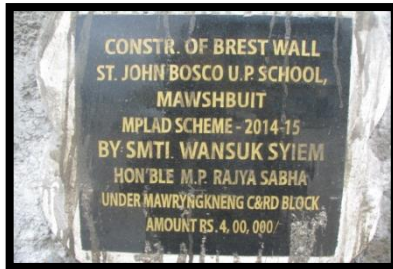
| | |
|---|--|
|  | |
| Date of Inspection | 15.07.2016 |
| Team of inspection officers | Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer |
| Accompanied by | Shri B. Nongsiej, Assistant Engineer. |
| Name of the Scheme: | Construction of St. Joseph L.P School, Lad Kynton-U-Mon, Lad Nongkrem |
| Name of the MP: | Shri V.H. Pala MP(LS) |
| Year recommended/sanctioned: | 2014-15 |
| Amount & Date of sanctioned by the DC: | Rs. 5,00,000/- sanctioned on 02 nd September 2015 |
| Reason for delay in sanction, if any: | Nil |
| Date of release of fund: 1st instalment :- | Rs. 2,50,000/- released from Block Office on 07 th September 2015 |
| Reason for delay in release of fund, if any: | Nil |
| Amount utilized: | Rs. 2,50,000/- |
| Date of commencement/starting of the work: | 03 rd November 2015 |
| Date of completion/Expected date of completion: | 31 st July 2016 |
| Status of the work: | In progress (85% completed) |
| Cause/Reason for delay in sanction/completion of works: | (a) The School Managing Committee was able to submit the relevant documents and resolution to the BDO's office on 02-11-2015 and fund for starting the project was released on the same day. |
| Whether inspection carried out from Block/DCs office: | Yes, at regular intervals from Block Office. |
| Name of executing agency: | The School Managing Committee, St. Joseph L.P School, Lad Kynton-U-Mon, Lad Nongkrem. |
| Whether signboard erected or not: | No |
| Date of submission of UC: 1st Instalment: | Not yet submitted by beneficiary. |
| In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC: | Yes. |
| Impact of the scheme: | The school building is an asset to the school in imparting better education. |
| Findings/Observations: | <ol style="list-style-type: none"> 1. The inspection team found the construction of school building is under progress. It is constructed with usage of good quality materials. 2. Structural work, fixing of window (steel casement window) is completed. 3. Internal and External plastering, block walling is in progress. 4. Its dimension, Plinth area, L=5.2m and B=4.6mVerandah, L=5.5 and B=1.2 Height of building, H=2.7m 5. It was informed that the School Managing Committee had contributed ₹ 1.50 lakh. 6. The members of the School Managing Committee were advised to submit the UC of the 1st installment so that the 2nd installment can be released. 6. The School Managing Committee was advised to erect the plaque with complete details after completion of the scheme. |
| Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation | - |
| Shri S. Sungoh, Research Officer Programme Implementation & Evaluation | - |
| Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | - |
| Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | - |

CONSTRUCTION OF PERMANENT STAGE AT MADAN IEW PYNSING, NONGKREM


| | |
|--|---|
|    | |
| Date of Inspection | 15.07.2016 |
| Team of inspection officers | Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer |
| Accompanied by | Shri B. Nongsiej, Assistant Engineer |
| Name of the Scheme: | Construction of Permanent Stage at Madan Iew Pynsing, Nongkrem |
| Name of the MP: | Shri V.H Pala MP(LS) |
| Year recommended/sanctioned: | 2014-15 |
| Amount & Date of sanctioned by the DC: | Rs. 5,00,000/- sanctioned on 14 th September 2015 |
| Reason for delay in sanction, if any: | Nil |
| Date of release of fund: 1 st instalment :- 2 nd instalment :- | Rs. 2,50,000/- released from Block Office on 30 th September 2015. Rs. 2,50,000/- released from Block Office on 13 th April 2015. |
| Reason for delay in release of fund, if any: | Nil |
| Amount utilized: | Rs. 5,00,000/- |
| Date of commencement/starting of the work: | 15 th September 2015 |
| Date of completion/Expected date of completion: | 10 th December 2015 |
| Status of the work: | Completed |
| Cause/Reason for delay in sanction/completion of works: | Nil |
| Whether inspection carried out from Block/DCs office: | Yes, at regular intervals from Block Office. |
| Name of executing agency: | Nongkrem Dorbar Pyllun, Nongkrem. |
| Whether signboard erected or not: | Yes |
| Date of submission of UC: 1 st Instalment: 2 nd Instalment: | Submitted to the BDO, Mawryngkneng C&RD Block on 03 rd March 2016. Not yet submitted to DC's office. |
| In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC: | No |
| Impact of the Scheme: | The permanent stage has helped the public while organizing various cultural programmes of Nongkrem village. |
| Findings/Observations: | 1. The inspection team found that the construction of permanent stage was constructed with usage of good quality materials and good workmanship. 2. Dimension of stage, L=6.3m, B= 3.2m and H=1m. 3. Railing grill, L=21m and H=0.35m. Apron: L=31m and B=0.60m. |
| | |
| Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation | - |
| Shri S. Sungoh, Research Officer Programme Implementation & Evaluation | - |
| Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | - |
| Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | - |

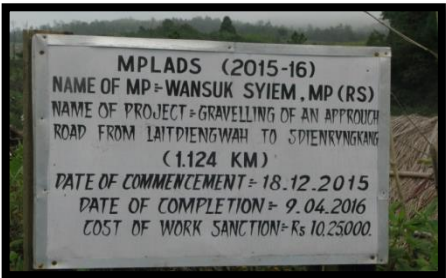


| CONSTRUCTION OF PLAYGROUND FOR SALEM EDUCATIONAL SOCIETY, KYNTON-U-MON. | |
|--|---|
|    | |
| Date of Inspection | 15.07.2016 |
| Team of inspection officers | Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer |
| Accompanied by | Shri B. Nongsiej, Assistant Engineer |
| Name of the Scheme: | Construction of Playground for Salem Educational Society, Kynton-U-Mon. |
| Name of the MP: | Smt. W. Syiem MP(RS) |
| Year recommended/sanctioned: | 2013-14 |
| Amount & Date of sanctioned by the DC: | Rs. 20,00,000/- sanctioned on 13 th August 2014 |
| Reason for delay in sanction, if any: | Nil |
| Date of release of fund: 1 st instalment :- 2 nd instalment :- | Rs. 10,00,000/- released from block office on 25 th September 2014 Rs. 10,00,000/- released from block office on 05 th March 2015 |
| Reason for delay in release of fund, if any: | Nil |
| Amount utilized: | Rs. 20,00,000/- |
| Date of commencement/starting of the work: | 22 nd October 2014 |
| Date of completion/Expected date of completion: | 24 th March 2015 |
| Status of the work: | Completed |
| Cause/Reason for delay in sanction/completion of works: | Nil |
| Whether inspection carried out from Block/DCs office: | Yes, at regular intervals from Block Office. |
| Name of executing agency: | Salem Educational Society, Kynton-U-Mon, Nongkrem |
| Whether signboard erected or not: | Yes |
| Date of submission of UC: 1 st Instalment: 2 nd Instalment: | Submitted to the BDO Mawryngkneng C&RD Block on 03 rd March 2016 Submitted to the BDO Mawryngkneng C&RD Block on 05 th June 2015 |
| In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC: | Yes |
| Impact of the Scheme: | The playground helps the school by promoting extracurricular activities for the students. |
| Findings/Observations: | 1. The inspection team found that the construction of playground including fencing and retaining wall was completed. 2. Dimension of a playground, L=82m and H=50m. Dimension of fencing, L=50m and H=1.5m. Dimension of Retaining Wall, L=58m and H=3m. |
| | |
| Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation | - |
| Shri S. Sungoh, Research Officer Programme Implementation & Evaluation | - |
| Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | - |
| Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | - |

CONSTRUCTION OF BREAST WALL AT ST. JOHN BOSCO U.P SCHOOL, MAWSHABUIT.



| | |
|---|---|
| Date of Inspection | 15.07.2016 |
| Team of inspection officers | Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer |
| Accompanied by | Shri B. Nongsiej, Assistant Engineer |
| Name of the Scheme: | Construction of Breast Wall at St. John Bosco U.P School, Mawshabuit. |
| Name of the MP: | Smt. W.Syiem MP(RS) |
| Year recommended/sanctioned: | 2015-16 |
| Amount & Date of sanctioned by the DC: | Rs.4,00,000/- sanctioned on 23 rd February 2015 |
| Reason for delay in sanction, if any: | Nil |
| Date of release of fund: 1st instalment :- 2nd instalment :- | Rs. 2,00,000/- released from block office on 01 st June 2015 Rs. 2,00,000/- released from block office on 05 th April 2016 |
| Reason for delay in release of fund, if any: | Nil |
| Amount utilized: | Rs. 4,00,000/- |
| Date of commencement/starting of the work: | 01 st August 2015 |
| Date of completion/Expected date of completion: | 18 th November 2015 |
| Status of the work: | Completed |
| Cause/Reason for delay in sanction/completion of works: | Nil |
| Whether inspection carried out from Block/DCs office: | Yes, at regular intervals from Block Office. |
| Name of executing agency: | The School Managing Committee, St. John Bosco U.P School, Mawshabuit. |
| Whether signboard erected or not: | Yes |
| Date of submission of UC: 1st instalment :- 2nd instalment :- | Submitted to the BDO, Mawryngkneng C&RD Block on 08 th January 2016 Not yet submitted to D.C's office. |
| In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC: | No |
| Impact of the Scheme: | (i) The breast wall has helped the school in having a proper permanent boundary. (ii) It also helps in avoiding landslide and mud flow in the school compound. |
| Findings/Observations: | 1. The inspection team found that the construction of breast wall is completed. It is constructed with usage of good quality material and good workmanship. Its length (L=50m and H=3m). 2. It was informed that out of the 50mtrs, 25mtrs of the wall was constructed as a social work in collaboration with the local people who contributed in cash and kind. |
| | |
| Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation | - |
| Shri S. Sungoh, Research Officer Programme Implementation & Evaluation | - |
| Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | - |
| Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | - |

| CONSTRUCTION OF MOTORABLE ROAD FROM MAWSIANG TO LUM SHNONG, RETAINING WALL, COMPOUND WALL, ETC., RNGIKSEH, NONGKREM | |
|--|--|
|  | |
| Date of Inspection | 15.07.2016 |
| Team of inspection officers | Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer |
| Accompanied by | Shri B. Nongsiej, Assistant Engineer |
| Name of the Scheme: | Construction of Motorable Road from Mawsiang to Lum Shnong, Retaining Wall, Compound Wall, etc., Rngikseh, Nongkrem |
| Name of the MP: | Smt. W.Syiem MP(RS) |
| Year recommended/sanctioned: | 2015-16 |
| Amount & Date of sanctioned by the DC: | Rs. 20,00,000/- sanctioned on 14 th July 2015 |
| Reason for delay in sanction, if any: | Nil |
| Date of release of fund: 1 st instalment :- 2 nd instalment :- | Rs. 10,00,000/- released from block office on 12 th August 2015 Not yet released. |
| Reason for delay in release of fund, if any: | Nil |
| Amount utilized: | Rs. 10,00,000/- |
| Date of commencement/starting of the work: | 28 th October 2015 |
| Date of completion/Expected date of completion: | 09 th April 2016 |
| Status of the work: | Completed |
| Cause/Reason for delay in sanction/completion of works: | Nil |
| Whether inspection carried out from Block/DCs office: | Yes, at regular intervals from Block Office. |
| Name of executing agency: | Rngikseh V.E.C, Rngikseh, Nongkrem. |
| Whether signboard erected or not: | No |
| Date of submission of UC: 1 st instalment :- 2 nd instalment :- | Submitted to the BDO, Mawryngkneng C&RD Block on 28 th April 2016 ----- |
| In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC: | No. |
| Impact of the Scheme: | The road has helped the residents of Rngikseh in their daily life especially during medical emergency and also for development of their locality where many residents can avail the motorable road. |
| Findings/Observations | <ol style="list-style-type: none"> The inspection team found that the construction of motorable road, R/W, Compound wall was constructed with usage of good quality materials and good workmanship. Its dimension: Motorable Road, L=65m and H= 5m. Retaining Wall, L=93.5m and H=1.5m. Compound Wall, L=84.7m and H=1m. Gate 1, L=3.9m and H=1.6m Gate 2, L=2.7m and H= 1.6m Gate 3, L=2.2m and H= 1.6m It was informed that the local community had contributed ₹ 3.00 Lakhs besides giving their land for the scheme. The members of the VEC were advised to take up the matter with the BDO for release of the 2nd installment. The local community was advised to erect a plaque with complete details. |
| Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation | - |
| Shri S. Sungoh, Research Officer Programme Implementation & Evaluation | - |
| Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | - |
| Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | - |

| GRAVELLING OF AN APPROACH ROAD FROM LAITDIENGWAH TO SDEINRYNGKANG. | |
|--|--|
|    | |
| Date of Inspection | 15.07.2016 |
| Team of inspection officers | Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdo, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer |
| Accompanied by | Shri B. Nongsiej, Assistant Engineer |
| Name of the Scheme: | Gravelling of an Approach Road from Laitdiengwah to Sdeinryngkang |
| Name of the MP: | Smt. W.Syiem MP(RS) |
| Year recommended/sanctioned: | 2015-16 |
| Amount & Date of sanctioned by the DC: | Rs. 10,25,000/- sanctioned on 27 th November 2015 |
| Reason for delay in sanction, if any: | Nil |
| Date of release of fund: 1 st instalment :- 2 nd instalment :- | Rs. 5,12,500/- released from block office on 11 th December 2015 Rs. 5,12,500/- released from block office on 05 th April 2016 |
| Reason for delay in release of fund, if any: | Nil |
| Amount utilized: | Rs. 10,25,000/- |
| Date of commencement/starting of the work: | 04 th January 2016 |
| Date of completion/Expected date of completion: | 31 st March 2016 |
| Status of the work: | Completed |
| Cause/Reason for delay in sanction/completion of works: | Nil |
| Whether inspection carried out from Block/DCs office: | Yes, at regular intervals from Block Office. |
| Name of executing agency: | Pynshongkhla V.E.C, Umphrup. |
| Whether signboard erected or not: | Yes |
| Date of submission of UC: 1 st instalment :- 2 nd instalment :- | Submitted to the BDO, Mawryngkneng C&RD Block on 10 th February 2016 Not yet submitted to D.C's Office. |
| In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC: | No |
| Impact of the Scheme: | The road has helped the farmers in the transportation of manure, fertilizer, agricultural produce, etc. |
| Findings/Observations: | <ol style="list-style-type: none"> 1. The inspection team found the construction of an approach road was completed.Its Length=1.124 km and Width=3m. 2. The V.E.C was advised to construct the side drain. 3. It was informed that due to insufficient amount of money, the construction of side drain and culvert cannot be carried out, the local committee (VEC) informed that the construction of side drain and culvert will be done from their own funds at the earliest. |

| | |
|---|---|
| Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation | - |
| Shri S. Sungoh, Research Officer Programme Implementation & Evaluation | - |
| Shri R.M.G Nongtdo, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | - |
| Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation | - |
