
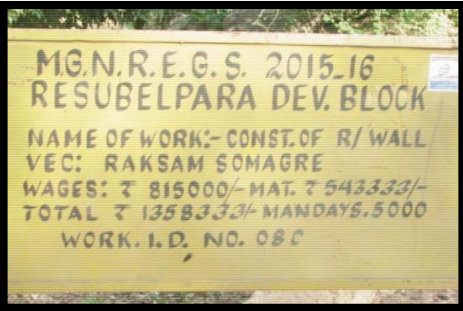





CONSTRUCTION OF ROAD FROM RONGSEP TO ACHUGRE	
	
Date of Inspection:	19 th January 2017
Team of inspection officers:	Shri S.Sungoh Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri L. Sangma, Junior Engineer, Resubelpara C &RD Block.
Name of the Scheme:	Construction of Road from Rongsep to Achugre
Name of the MP:	Shri P.A. Sangma, Ex- MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/-
Reason for delay of sanction, if any:	Nil
Amount & Date of release of fund: 1 st instalment :- 2 nd instalment :- 3 rd instalment :-	Rs. 3,00,000/- Rs. 1,25,000/- Rs. 75,000/-
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	NA
Date of completion/Expected date of completion:	NA
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	---
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by contractor, Shri Jonet Sangma.
Whether signboard erected or not:	No signboard
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	NA NA
In case of completed Scheme whether the completion Report/ Certificate submitted to BDO/DC:	Yes
Impact of the scheme:	The road has benefited in connecting from one village to another.
Findings/Observations:	<ol style="list-style-type: none"> 1. The inspection team found that the construction of the road is completed and the length of Kutcha road is 3 Km (approx) connecting the two villages, Rongsep and Achugre . 2. Its dimension: Length =3 Km and Roadway width=6m. Kutcha side drain= 0.06m*0.06m, Both side. 3. It was found that the road is good. 4. The Junior Engineer, Resubelpara C&RD Block has been advised to inform the executing agency to submit the Utilisation Certificate and completion Certificate to the Block Office at the earliest. 5. It was informed that the signboard has already erected, but it has been remove by unknown person. So the Junior Engineer was advised to inform the executing agency to erect a new signboard with completed details.


RECONSTRUCTION OF RCC BRIDGE AT GOSINGPITA


  	
Date of Inspection:	19 th January 2016
Team of inspection officers:	Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri L. Sangma, Junior Engineer, Resubelpara C & RD Block.
Name of the Scheme:	Reconstruction of RCC Bridge at Gosingpita
Name of the MP:	Shri P.A. Sangma, Ex- MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs 10,00,000/-
Reason for delay in sanction, if any:	Nil
Amount & Date of release of fund: 1 st instalment :- 2 nd instalment :- 3 rd instalment :-	Rs. 6,00,000/- Rs. 2,50,000/- Rs. 1,50,000/-
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 10,00,000/-
Date of commencement/starting of the work:	NA
Date of completion/Expected date of completion:	NA
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by Contractor, Shri Silkam Sangma.
Whether signboard erected or not:	No signboard.
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	Submitted to BDO, Resubelpara C&RD Block on 07 th January 2015.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	-----
Impact of the scheme:	Benefits for connection one village to another village.
Findings/Observations:	<ol style="list-style-type: none"> On inspection it was found that the construction of RCC Bridge is completed. Its dimension: Span(L)= 16.9m and W=2.90m. Parapet Railing (L) = 17m and H= 0.85m Wingwall (1) L= 6.7m and H=2m Wingwall (2) L=6m and H=2.8m Wingwall (3) L=4.2m and H=2.9m Wingwall (4) L=3.1m and H=3.5m Abutment (1) L=1.55m, B=1.60m and H=3.3m Abutment (2) L= 1.55m, B= 1.60m and H=3.3m Longitudinal Girder : H=0.5m, W=0.4m and L=16.9m It was informed by the Junior Engineer that the work was converging with MGNREGS as a labour wages. The inspection team found out that the fund of the scheme was well utilized and also well constructed. The structure of the RCC Bridge was good and strong. The Junior Engineer was advised to inform the executing agency to erect a plaque with complete details.

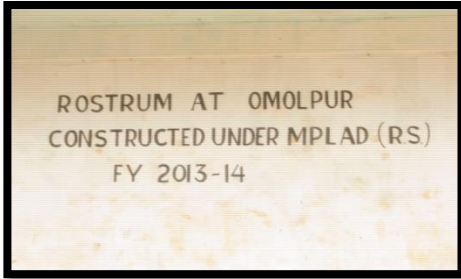


CONSTRUCTION OF RCC ROSTRUM AT OMOLPUR





Date of Inspection:	19 th January 2017
Team of inspection officers:	Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri L. Sangma, Junior Engineer, Resubelpara C & RD Block
Name of the Scheme:	Construction of RCC Rostrum at Omolpur
Name of the MP:	Smt Wansuk Syiem, MP(RS)
Year recommended/sanctioned:	2013-14
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/-
Reason for delay in sanction, if any:	Nil
Amount & Date of release of fund: 1st instalment :- 2nd instalment :- 3rd instalment :-	Rs. 3,75,000/- Rs. 1,25,000/-
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	NA
Date of completion/Expected date of completion:	NA
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	---
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Secretary, Village Committee,
Whether signboard erected or not:	No signboard
Date of submission of UC: 1st Instalment: 2nd Instalment:	NA NA
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Submitted to BDO.
Impact of the scheme:	Availability of Rostrum has helped the village to organising various cultural programs.
Findings/Observations:	<ol style="list-style-type: none"> The inspection was carried out in presence of Committee Members of the locality. It was observed that the construction of Rostrum attached with toilet is completed and already utilised by the village in various cultural programs Its dimension: Stage : L=5.9m, B=3.9m and H=1.2m Colum Size : 26cm*25cm*260cm Beam Size : 30cm*25cm*420cm Wall : L=580cm and H=250cm 2 No's of step: Thread=30cm , Rises=16cm and Width = 1.50cm. Toilets : L=2m, B=2m and H=2.5m Door : B=80cm and H=180cm Chowkat : 470cm*10cm*6cm Septic Tank : L= 1.80m, H=1.8m and B=1.30m Slab : Thickness = 10cm, L=5.7m and B=3.9m The Junior Engineer has been advised to inform the executing agency to erect a signboard with complete details.

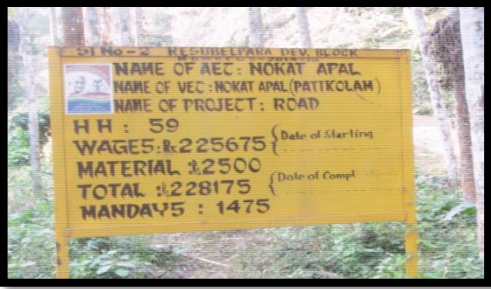
CONSTRUCTION OF BUILDING YOUTH CENTER CUM CONGRESS HALL AT BELPARA	
	
Date of Inspection:	19 th January 2017
Team of inspection officers:	Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri L. Sangma, Junior Engineer, Resubelpara C &RD Block
Name of the Scheme:	Construction of Building Youth Centre Cum Congress Hall at Belpara
Name of the MP:	Shri P.A. Sangma, Ex- MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 20,00,000/-
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :- 3 rd instalment :-	Rs. 12,00,000/- Rs. 5,00,000/- Not yet released
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 17,00,000/-
Date of commencement/starting of the work:	NA
Date of completion/Expected date of completion:	NA
Status of the work:	Work in progress.
Cause/Reason for delay in sanction/completion of works:	---
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by Shri Debinson Marak
Whether signboard erected or not:	---
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	NA NA
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Submitted to BDO.
Impact of the scheme:	Benefits for the local people for their various needs, like awareness programs, awards ceremonies, etc.
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction is under progress. The structural work is completed whereas flooring and walling are yet to be started. Its dimension: Plinth area : L=23m and B=9.5m Plinth Height : 50cm Column Size : 30cm*33cm*300cm Necessary steps should be taken by the BDO for submission of Utilisation Certificate by the beneficiaries. The Junior Engineer was advised to fix a plaque on the wall of the building indicating the details viz., Name of scheme, Name of MP, Year, Amount sanctioned, date of commencement and date of completion etc. after the scheme is completed.


CONSTRUCTION OF MOTORABLE ROAD FROM CHIDARET TO DAME	
	
Date of Inspection:	19 th January 2017
Team of inspection officers:	Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri L. Sangma, Junior Engineer, Resubelpara C & RD Block.
Name of the Scheme:	Construction of Motorable Road from Chidaret to Dame
Name of the MP:	Shri P.A. Sangma, Ex-MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/-
Reason for delay in sanction, if any:	Nil
Amount & Date of release of fund: 1 st instalment :- 2 nd instalment :- 3 rd instalment :-	Rs. 3,00,000/- Rs. 1,25,000/- Rs. 75,000/-
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	NA
Date of completion/Expected date of completion:	NA
Status of the work:	completed
Cause/Reason for delay in sanction/completion of works:	---
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by Shri Silkam Sangma Chidaret
Whether signboard erected or not:	No signboard
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	NA NA
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Submitted to BDO.
Impact of the scheme:	Benefits for transportations of people and goods from village to other
Findings/Observations:	<ol style="list-style-type: none"> 1. On inspection the team found that the construction is completed. 2. Its dimension: Kutchra Road : Length =3km and Roadway width=6m 3. It was informed that earlier the scheme was on MP Scheme and at present it has been hand over to PMGSY for up-gradation. 4. Necessary steps should be taken by BDO/Junior Engineer for submission of Utilisation Certificate in time and fixing the Plaque when the construction is completed.



CONSTRUCTION AND IMPROVEMENT OF ROAD FROM KONGKAL TO NOKAT	
  	
Date of Inspection:	19 th January 2017
Team of inspection officers:	Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri L. Sangma, Junior Engineer, Resubelpara C &RD Block.
Name of the Scheme:	Construction and Improvement of Road from Kongkal to Nokat
Name of the MP:	Shri P.A. Sangma, Ex- MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/-
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :- 3 rd instalment :-	Rs. 3,00,000/- Rs. 1,25,000/- Rs. 75,000/-
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	NA
Date of completion/Expected date of completion:	NA
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	---
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by Shri Chalchang Sangma
Whether signboard erected or not:	No signboard
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	NA NA
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Submitted to BDO.
Impact of the scheme:	Benefits for transportations of people and goods from village to other
Findings/Observations:	<ol style="list-style-type: none"> 1. It was found that the construction and improvement of road are completed. 2. Its dimension: Kutchra Road : Length =4.5km and Roadway width=6m 3. It was informed that the work was converging with MGNREGS as a labour wages. 4. There was no plaque and therefore the Junior Engineer was advised to inform the Executing Agency to fixed a plaque indicating the Name of MP, Year, Name of scheme, Amount sanctioned, date of commencement and date of completion, etc

CONSTRUCTION OF MOTORABLE ROAD FROM TEKALANG TO SONGGITAL	
	
Date of Inspection:	19 th January 2017
Team of inspection officers:	Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri L. Sangma, Junior Engineer, Resubelpara C&RD Block.
Name of the Scheme:	Construction of Motorable Road from Tekalang to Songgital
Name of the MP:	Shri P.A. Sangma, Ex- MP(LS)
Year recommended/sanctioned:	2015-16
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/-
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1st instalment :- 2nd instalment :-	Rs. 3,00,000/- Rs. 2,00,000/-
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	NA
Date of completion/Expected date of completion:	NA
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by Shri Dickey M. Momin
Whether signboard erected or not:	No signboard
Date of submission of UC: 1st Instalment: 2nd Instalment:	Submitted to BDO, Resubelpara C&RD Block on 01 st March 2016
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Submitted to BDO.
Impact of the scheme:	Benefits for transportations of people and goods from village to other
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of Motorable road is completed but no side drainage has been carried out along the road to prevent the surface of the road from deteriorating in the upcoming monsoon season. Its dimension: Kutcha Road : Length L=4.5km and Roadway width=6m No signboard was erected, therefore, BDO/Junior Engineer should instructed the beneficiaries to fix the plaque when the work is completed.

CONSTRUCTION OF MOTORABLE ROAD FROM DARAM SONGMA TO SONGGITAL AND ADINGGRE	
	
Date of Inspection:	19 th January 2017
Team of inspection officers:	Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri L. Sangma, Junior Engineer, Resubelpara C&RD Block.
Name of the Scheme:	Construction of Motorable Road from Daram Songma to Songgital and Adinggre
Name of the MP:	Shri P.A. Sangma, Ex- MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/-
Reason for delay in sanction, if any:	Nil
Amount & Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 3,00,000/- Rs. 2,00,000/-
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	NA
Date of completion/Expected date of completion:	NA
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Village committee
Whether signboard erected or not:	No signboard
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	NA NA
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Submitted to BDO.
Impact of the scheme:	Benefits for transportations of people and goods from village to other
Findings/Observations:	<ol style="list-style-type: none"> The inspection team found that the construction of Motorable road is completed. Its dimension: Kutcha Road : Length=4.5km and Roadway width=6m Kutcha Sides Drain size : 60cm*60cm. The Junior Engineer was advised to inform the village committee to erect a signboard with complete details.

CONSTRUCTION OF MOTORABLE ROAD FROM CHIDARET TO BOKMA	
	
Date of Inspection:	19 th January 2017
Team of inspection officers:	Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri L. Sangma, Junior Engineer, Resubelpara C&RD Block
Name of the Scheme:	Construction of Motorable Road from Chidaret to Bokma
Name of the MP:	Shri P.A. Sangma, Ex- MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/-
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 3,00,000/- Rs. 2,00,000/-
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	NA
Date of completion/Expected date of completion:	NA
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by Shri Dickey M. Momin
Whether signboard erected or not:	No signboard
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	NA NA
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Submitted to BDO.
Impact of the scheme:	Benefits for transportations of people and goods from village to other
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of Motorable road is completed. Its dimension: Kutchia Road : Length=4.5km and Roadway width=6m The Junior Engineer has been advised to inform the Executing Agency to furnish the Utilisation Certificate to the BDO at the earliest and also to erect the signboard mentioning the name of the scheme, name of MP, amount sanctioned and year of sanction etc within a week.

CONSTRUCTION OF MOTORABLE ROAD FROM DARAM VILLAGE TO RONGMATCHA	
	
Date of Inspection:	19 th January 2017
Team of inspection officers:	Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri L. Sangma, Junior Engineer, Resubelpara C&RD Block
Name of the Scheme:	Construction of Motorable Road from Daram Village to Rongmatcha
Name of the MP:	Shri P.A. Sangma, Ex- MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/-
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 3,00,000/- Rs. 2,00,000/-
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	NA
Date of completion/Expected date of completion:	NA
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by Shri Silkam Sangma
Whether signboard erected or not:	No signboard
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	NA NA
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Submitted to BDO.
Impact of the scheme:	Benefits for transportations of people and goods from village to other
Findings/Observations:	<ol style="list-style-type: none"> 1. It was observed that the construction of Motorable road is completed but no side drainage has been carried out along the road to prevent the surface of the road from deteriorating in the upcoming monsoon season. 2. Its dimension: Katcha Road : Length=3.5km and Roadway width=6m 3. The Junior Engineer was advised to inform the committee to erect a permanent signboard indicating the name of the scheme, name of MP, amount sanctioned, year of sanction, Date of commencement and Date of Completion etc within a week.

CONSTRUCTION OF MOTORABLE ROAD FROM BANGALMURA TO RESERVE GITTIM	
 	
Date of Inspection:	19 th January 2017
Team of inspection officers:	Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri L. Sangma, Junior Engineer, Resubelpara C&RD Block
Name of the Scheme:	Construction of Motorable Road from Bangalmura to Reserve Gittim
Name of the MP:	Shri P.A. Sangma, EX- MP(LS)
Year recommended/sanctioned:	2015-16
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/-
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :- 3 rd instalment :-	Rs. 3,00,000/- Rs. 1,25,000/- Rs. 75,000/- released from block office on
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	NA
Date of completion/Expected date of completion:	NA
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by Shri Dickey M. Momin
Whether signboard erected or not:	No signboard
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	Submitted to BDO, Resubelpara C&RD Block on 03 rd January 2016
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Submitted to BDO.
Impact of the scheme:	Benefits for transportations of people and goods from village to other
Findings/Observations:	<ol style="list-style-type: none"> 1. It was found that the construction of Motorable road is completed. 2. Its dimension: Kutchra Road : Length =2.5km and Roadway width=6m 3. The Junior Engineer is requested to take regular supervision/inspection of any work undertaken to ensure quality of the work and also instruction should be given to the executing agency for construction the side drain along the road to prevent the surface of the road from the upcoming monsoon season. 4. Necessary action should be taken by the BDO to ensure erecting of the signboard mentioning the name of the scheme, name of MP, amount sanctioned, year of sanction, Date of commencement and Date of Completion etc when the work is completed
