

CONSTRUCTION OF APPROACH ROAD AT MAWRANG VILLAGE



Date of Inspection	19 th April 2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri P. Warjri, Sectional Assistant, Mairang C & RD Block and Shri P. Lyngdoh, Gram Sevak, Mairang C & RD Block
Name of the Scheme:	Construction of Approach road at Mawrang
Name of the MP:	Smt. W. Syiem MP(RS)
Year recommended/sanctioned:	2015-16
Amount & Date of sanctioned by the DC:	Rs. 6,00,000/- sanctioned on 1-12-2015
Date of release of fund: 1st instalment :- 2nd instalment :-	Released from Block Office on 28-3-2016 Not yet released from Block Office.
Amount utilized:	Rs. 4,50,000/-
Date of commencement/starting of the work:	28-3-2016
Status of the work:	Under progress
Whether inspection carried out from Block/DCs office:	Yes
Name of executing agency:	The work is executed by Mawthadraishan People Welfare & Dev. Organisation Kynshi
Whether signboard erected or not:	No.
Date of submission of UC:	Utilisation Certificate of 1 st instalment has been submitted to BDO, Mairang C & RD Block on 28-3-2016.
Findings/Observations	<p>1. On inspection it was found that road construction is under progress.</p> <p>2. The Sectional Assistant looking after the MPLADS works and Gram Sevak of the concerned circle was advised to inform the Executing Agency to excavate proper drainage for the improvement of the road and also to erect the signboard after the work is completed.</p> <p>3. For cross drainage a Hume pipe was laid whose Outer Dia. is 1.20M and Inner Dia. 1.00M</p>
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

CONSTRUCTION OF ROAD FROM PWD ROAD MAWKOHMIT TO NONGRANG VILLAGE



Date of Inspection	19 th April 2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri P. Warjri, Sectional Assistant, Mairang C & RD Block and Shri P. Lyngdoh, Gram Sevak, Mairang C & RD Block
Name of the Scheme:	Construction of Road from PWD Road Mawkohmit to Nongrang Village (1km approx)
Name of the MP:	Smt. W. Syiem MP(RS)
Year recommended/sanctioned:	2015-16
Amount & Date of sanctioned by the DC:	Rs 5,00,000/- sanctioned on 1-12-2015
Date of release of fund:	
1st instalment :-	Released from Block Office on 28-3-2016
2nd instalment :-	Not yet released from Block Office.
Amount utilized:	Rs.3,75,000/-
Date of commencement/starting of the work:	28-3-2016
Status of the work:	Under progress
Whether inspection carried out from Block/DCs office:	Yes
Name of executing agency:	The work is executed by Mawthadraishan People welfare & Dev. Organisation Kynshi
Whether signboard erected or not:	Not yet Erected.
Date of submission of UC:	Utilisation Certificate of 1 st instalment has been submitted to BDO, Mairang C & RD Block on 28-3-2016
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	
Findings/Observations	<p>1. It was found that road construction i.e. site clearance, Right of way , clearing width and roadway is complete but side drainage is yet to be carried out.</p> <p>2. The Sectional Assistant looking after the MPLADS works and Gram Sevak of the concerned circle was advised to inform the executing agency to complete the drainage so as to prevent the surface of the road from deteriorating in the upcoming monsoon season and also to erect the signboard after the work is completed</p>

Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-


CONSTRUCTION OF ROAD INCLUDING HOME PIPES FROM SOHPHOH MAWLONG TO MAWKHAPKHWHA



Date of Inspection	19 th April 2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri P. Warjri, Sectional Assistant, Mairang C & RD Block and Shri P. Lyngdoh, Gram Sevak, Mairang C & RD Block
Name of the Scheme:	Construction of road including Home pipes from Sohphoh Mawlong to Mawkhaphkwa (3 kms approx)
Name of the MP:	Smt. W. Syiem MP(RS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 9,00,000/- sanctioned on 21-1-2015
Date of release of fund: 1st instalment :- 2nd instalment :-	Released from Block Office on 10-4-2015 Not yet released from Block Office.
Amount utilized:	6,75,000/-
Date of commencement/starting of the work:	10-4-2015
Status of the work:	Under progress
Whether inspection carried out from Block/DCs office:	Yes
Name of executing agency:	The work is executed by Mawthadraishan People welfare & Dev. Organisation Kynshi
Whether signboard erected or not:	No
Date of submission of UC:	1 st instalment has been submitted to the BDO, Mairang C&RD Block on 10-4-2015
Findings/Observations	<ol style="list-style-type: none"> 1. The inspection team was informed by the Sectional Assistant that the road is an existing road and improvement work was to be carried out to make the road better. 2. The inspection team found that condition of the road was not up-to the mark. Apart from that, there was no construction of side drain which had led to deterioration of the surface especially during rainy season leaving the road in very bad condition leading to deep scours on the surface of the road. 3. The Sordar of the village has also complained about the condition of the road which was very bad, especially during monsoon reason as there is no proper side drainage 4. The Sectional Assistant was advised to inform the BDO, Mairang not to release the 2nd instalment until such time the side drainage work has been carried out. The members of the beneficiary Organisation who also accompanied the inspection team were apprised of the situation and told to take corrective measures before availing the 2nd instalment.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
--	---

CONSTRUCTION OF BOUNDARY FENCING OF LAITDOM HIGHER SECONDARY SCHOOL, MAWILIEH LAITDOM



Date of Inspection	19 th April 2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri P. Warjri, Sectional Assistant of Mairang C & RD Block and Shri P. Lyngdoh, Gram Sevak, Mairang C & RD Block

Name of the Scheme:	Construction of Boundary fencing of Laitdom Higher Secondary School, Mawlieh Laitdom
Name of the MP:	Smt. W. Syiem MP(RS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 21-1-2015
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Released from Block Office on 23-7-2015 Not yet released from Block Office.
Amount utilized:	Rs. 3,75,000/-
Date of commencement/starting of the work:	23-7-2015
Date of completion/Expected date of completion:	Not yet completed
Status of the work:	About to complete
Whether inspection carried out from Block/DCs office:	Yes
Name of executing agency:	The work is executed by the Managing committee Laitdom Presbyterian Secondary School Mawlieh
Whether signboard erected or not:	Erected
Date of submission of UC:	1 st instalment has been submitted to the BDO,Mairang C&RD Block on 23-7-2015

Findings/Observations	1.The inspection team found that the boundary fencing was well constructed, durable with good quality materials being used. 2.The fencing at Laitdom Secondary School was 95% completed and some portion of the wall is still remaining to be constructed and its length is more than 110 meter approx including Retaining Wall. 3.The Secretary, Managing Committee Laitdom Presbyterian Secondary School Mawlieh informed that to expedite early completion of the work the Committee had spent from the School funds to complete the construction while awaiting the 2 nd installment from the Block Office.
-----------------------	--


Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

CONSTRUCTION OF HALL AT ST. THOMAS HIGHER SECONDARY SCHOOL PYNDENGUMIONG, MAIRANG



Date of Inspection	19 th April 2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri P. Warjri, Sectional Assistant, Mairang C & RD Block and Shri P. Lyngdoh, Gram Sevak, Mairang C & RD Block
Name of the Scheme:	Construction of Hall at St. Thomas Higher Sec. School, Mairang
Name of the MP:	Shri. V.H. Pala, MP(LS)
Year recommended/sanctioned:	2013-14
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 24-10-2013
Date of release of fund: 1st instalment :- 2nd instalment :-	Released from Block Office on 3-3-2014 Not yet released from Block Office.
Amount utilized:	Rs. 3,71,250/-
Date of commencement/starting of the work:	3-3-2014
Status of the work:	Under progress
Whether inspection carried out from Block/DCs office:	Yes
Name of executing agency:	The work is executed by Managing Committee of St. Thomas Higher Secondary School , Mairang.
Whether signboard erected or not:	No
Date of submission of UC:	Utilisation Certificate of 1 st instalment has been submitted to the BDO,Mairang C&RD Block on 3-3-2014
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Findings/Observations	<ol style="list-style-type: none"> 1. The inspection team found that the Hall was constructed up to plinth level and is under progress. It was observed that the amount sanction is insufficient as the Hall structure is huge and additional funding is required for its completion. 2. The Secretary, School Managing Committee informed that the project costs almost Rs 50.00 lakhs and school funds have been utilised for Construction of the Hall. 3. The Sectional Assistant who is looking after MPLADS works was advised to release the 2nd installment as soon as possible so as to facilitate the construction, since the amount sanctioned by the MP is very small compared to the project cost.
Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-


EXTENSION OF MAIRANG PRESBYTERIAN SCIENCE COLLEGE, MAIRANG

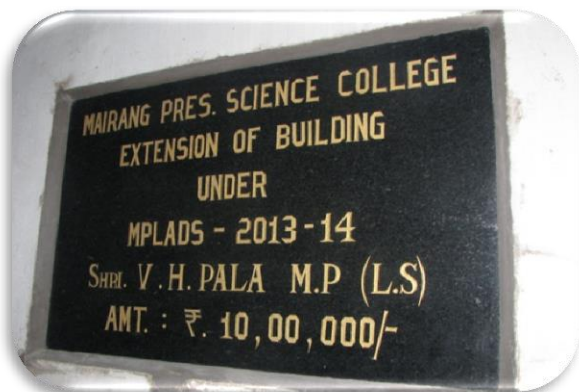

Date of Inspection	19 th April 2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri P. Warjri, Sectional Assistant, Mairang C & RD Block and Shri P. Lyngdoh, Gram Sevak, Mairang C & RD Block
Name of the Scheme:	Extension of Mairang Presbyterian Science college building. Mairang
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2013-14
Amount & Date of sanctioned by the DC:	Rs.10,00,000/- sanctioned on 24-10-2013
Date of release of fund: 1st instalment :- 2nd instalment :-	Released from Block Office on 3-3-2014 Not yet released from Block Office
Amount utilized:	Rs. 7,42,500/-
Date of commencement/starting of the work:	3-3-2014
Date of completion/Expected date of completion:	December, 2015
Status of the work:	Completed
Whether inspection carried out from Block/DCs office:	Yes
Name of executing agency:	Governing Body Mairang Presbyterian Science college
Whether signboard erected or not:	Yes
Date of submission of UC: 1st instalment :- 2nd instalment :-	Submitted to the BDO,Mairang C&RD Block on 3-3-2014 Not yet released.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Findings/Observations	<ol style="list-style-type: none"> 1. The inspection team found that the work is completed and the building is being utilized as class rooms, etc. and the quality of construction is very good. 2. Governing Body Mairang Presbyterian Science College informed that the 2nd instalment is yet to be received from the Block Office and they had spent from the School funds for completion of the College Building. 3. The Sectional Assistant who is looking after MPLADS works was advised to release the 2nd installment as soon as possible after completion of formalities.

Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

CONSTRUCTION OF SCHOOL BUILDING & PURCHASE OF COMPUTERS OF NONGRIMAI SECONDARY SCHOOL, NONGRIMAI



Date of Inspection	19 th April 2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri P. Warjri, Sectional Assistant, Mairang C & RD Block and Shri P. Lyngdoh, Gram Sevak, Mairang C & RD Block
Name of the Scheme:	Construction of School building & Purchase of Computers of Nongrimai Secondary School
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2013-14
Amount & Date of sanctioned by the DC:	Rs. 7,50,000/- sanctioned on 24-10-2013
Date of release of fund: 1st instalment :- 2nd instalment :- 3rd instalment :-	Released from Block Office on 31-1-2014 Released from Block Office on 2-4-2015 Released from Block Office on 22-2-2016
Amount utilized:	Rs. 7,50,000/-
Date of commencement/starting of the work:	31-1-2014
Date of completion/Expected date of completion:	December, 2016
Status of the work:	Completed
Whether inspection carried out from Block/DCs office:	Yes
Name of executing agency:	The work is executed by the Managing Committee Nongrimai Secondary School, Nongrimai
Whether signboard erected or not:	Yes
Date of submission of UC: 1st instalment :- 2nd instalment :-	Submitted to BDO, Mairang C&RD Block on 31-1-2014 Submitted to BDO, Mairang C&RD Block on 22-2-2016
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Findings/Observations	<ol style="list-style-type: none"> 1. The inspection team found that the School Building was completed and all the equipment at the school premises were available. There are 5 Computers & 1 printer, 3 Computer tables and 5 chairs which were used by the students of the School. 2. There are two rooms whereby one room has been utilized as a classroom and the other as a Computer room. The Plinth area of the Building = 64.64sqm.

Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

CONSTRUCTION OF BOUNDARY FENCING OF MANAI SECONDARY SCHOOL



Date of Inspection	19 th April 2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri P. Warjri, Sectional Assistant, Mairang C & RD Block and Shri P. Lyngdoh, Gram Sevak, Mairang C & RD Block
Name of the Scheme:	Construction of Boundary fencing of Manai Secondary School, Manai
Name of the MP:	Smt. W. Syiem MP(RS)
Year recommended/sanctioned:	2013-14
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 9-1-2014
Date of release of fund:	
1 st instalment :-	Released from Block Office on 11-5-2015
2 nd instalment :-	Released from Block Office on 11-3-2016
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	11-5-2015
Date of completion/Expected date of completion:	February, 2015
Status of the work:	Completed
Whether inspection carried out from Block/DCs office:	Yes
Name of executing agency:	The work is executed by the Managing Committee Manai Secondary School, Manai
Whether signboard erected or not:	Erected
Date of submission of UC:	
1 st instalment :-	Submitted to the BDO, Mairang C & RD Block on 11-5-2015
2 nd instalment :-	Submitted to the BDO, Mairang C & RD Block on 11-3-2016
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Findings/Observations	<ol style="list-style-type: none"> 1. The inspection team found that the boundary fencing at the school premises was completed. It is constructed with good quality and durable materials. Since, it is on the side of the National Highway road, adequate care has been taken to make it strong and sturdy to provide safety for the students from any accidents. Etc and also as a boundary of the School Campus. 2. Its length is 110 meter (approx) including retaining wall.

Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

EXTENSION OF MAIRANG PRESBYTERIAN ENGLISH SECONDARY SCHOOL, MAIRANG



Date of Inspection	19 th April 2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri P. Warjri, Sectional Assistant, Mairang C & RD Block and Shri P. Lyngdoh, Gram Sevak, Mairang C & RD Block

Name of the Scheme:	Extension of Mairang Presbyterian English Secondary School Mairang
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2012-13
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 25-06-2014
Date of release of fund:	
1st instalment :-	Released from Block Office on 10-2-2016
2nd instalment :-	-
Amount utilized:	3,71,250/-
Date of commencement/starting of the work:	10-2-2016
Date of completion/Expected date of completion:	
Status of the work:	Under progress
Whether inspection carried out from Block/DCs office:	Yes
Name of executing agency:	The work is executed by the Managing Committee Mairang Presbyterian English Secondary School, Mairang
Whether signboard erected or not:	Not yet erected.
Date of submission of UC:	
1st instalment :-	Submitted to BDO, Mairang C&RD Block 10-2-2016
2nd instalment :-	Not yet released
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	
Findings/Observations	<ol style="list-style-type: none"> 1. The inspection team found that the school building is under progress. The reason for delay in sanction is due to the objection of the Deputy Inspector of School West Khasi Hills. As per direction of the DI, the school shall not be less than 1 Km from another school. Hence, the school has been shifted to a new location for construction and as of now it is under progress. 2. The Sectional Assistant who is looking after MPLADS works was advised to release the 2nd installment as soon as possible to facilitate the construction.

Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-


CONSTRUCTION/EXTENSION OF ST. FRANCIS XAVIER SCHOOL AT NONGKHLAW



Date of Inspection	19 th April 2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri P. Warjri, Sectional Assistant, Mairang C & RD Block and Shri P. Lyngdoh, Gram Sevak, Mairang C & RD Block
Name of the Scheme:	Construction / Extension of St. Francis Xavier School at Nongkhlaw
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2011-12
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 1-08-2012
Date of release of fund: 1st instalment :- 2nd instalment :-	Released from Block Office on 03-10-2012 Released from Block Office on 31-01-2014
Amount utilized:	Rs. 4,95,000/-
Date of commencement/starting of the work:	03-10-2012
Date of completion/Expected date of completion:	December, 2013
Status of the work:	Completed
Whether inspection carried out from Block/DCs office:	Yes
Name of executing agency:	M/c St. Francis Xavier School Nongkhlaw
Whether signboard erected or not:	Not Erected
Date of submission of UC: 1st instalment :- 2nd instalment :-	03-10-2012 31-01-2014
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	No
Findings/Observations	<ol style="list-style-type: none"> 1. Onsite inspection at St. Francis School it was found that the extension/ construction of the school building was completed. The construction is utilized for 2 classrooms. 2. The rooms were well constructed and good quality materials were used as seen during the inspection. Its dimensions are 9.40M x 7.00M x 3.00M. 3. It was informed by the Sectional Assistant that the remaining amount of Rs 5000/- still pending with the BDOs office is due to non erection of the plaque/signboard. In this regard the School Managing Committee has been apprised to construct the plaque/signboard at the earliest possible and draw the remaining amount after completion of formalities.

Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L Jyrwa, Junior Engineer	-

CONSTRUCTION OF MAIRANG PRESBYTERIAN SCIENCE COLLEGE, MAIRANG

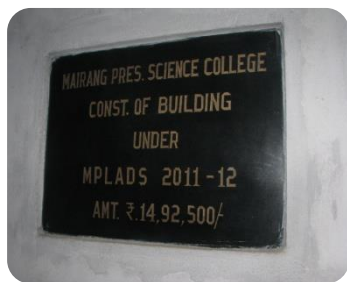

Date of Inspection	19 th April 2016
Team of inspection officers	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by	Shri P. Warjri, Sectional Assistant, Mairang C & RD Block and Shri P. Lyngdoh, Gram Sevak, Mairang C & RD Block
Name of the Scheme:	Construction of Mairang Presbyterian Science College Mairang
Name of the MP:	Shri V.H.Pala, MP(LS)
Year recommended/sanctioned:	2011-12
Amount & Date of sanctioned by the DC:	Rs. 14,92,500/- sanctioned on 1-11-2011
Date of release of fund: 1st instalment :- 2nd instalment :-	Released from Block Office on 8-12-2011 Released from Block Office on 29-10-2012
Amount utilized:	Rs. 14,92,500/-
Date of commencement/starting of the work:	8-12-2011
Date of completion/Expected date of completion:	September, 2012
Status of the work:	Completed
Whether inspection carried out from Block/DCs office:	Yes
Name of executing agency:	The work is executed by the Governing body Mairang Presbyterian Science college Mairang
Whether signboard erected or not:	Yes
Date of submission of UC: 1st instalment :- 2nd instalment :-	Submitted to BDO, Mairang C&RD Block on 8-12-2011 Submitted to BDO, Mairang C&RD Block on 29-10-2012
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Findings/Observations	<ol style="list-style-type: none"> 1. Onsite inspection it was observed that the construction of the building was completed and the Building is well constructed with a good quality materials. 2. The rooms constructed were used as Principals Room and 4 classrooms were made by partitioning 2 halls which were used by the students.

Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

