



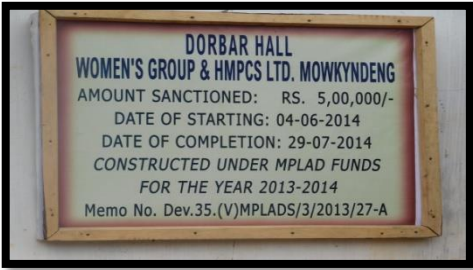




CONSTRUCTION OF SCHOOL BUILDING OF SAW LYNGDOH HIGHER SECONDARY SCHOOL, MOOKAIAW	
  	
Date of Inspection:	26.05.2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri P. Shullai, Assistant Engineer, Shri D. Chullet, Junior Engineer, Shri S. Law, Junior Engineer, Shri P. Wann, Gram Sevak, Shri M. Suchiang, Gram Sevak, and Shri B. Sutnga, Gram Sevak.
Name of the Scheme:	Construction of school building of Saw Lyngdoh Higher Secondary School, Mookaiaw
Name of the MP:	Shri V.H. Pala, MP(LS)
Year recommended/sanctioned:	2013-14
Amount & Date of sanctioned by the DC:	Rs. 10,00,000/- sanctioned on 6 th May 2014
Reason for delay of sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 5,00,000/- released from Block Office on 14 th April 2014. Rs. 5,00,000/- released from Block Office on 27 th May 2015.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 10,00,000/-
Date of commencement/starting of the work:	16 th April 2014
Date of completion/Expected date of completion:	16 th June 2015
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the School Managing Committee
Whether signboard erected or not:	Signboard erected without the name of MP
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	Submitted to BDO, Laskein C&RD Block on 12 th May 2015 -----
In case of completed Scheme whether the completion Report/ Certificate submitted to BDO/DC:	Yes
Impact of the scheme:	Construction of School building will have a positive impact on both students and community, high academic standards, teacher motivation and higher student achievements, etc
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of school building was completed (included with the purchasing of benches and tables). The team found that the building consists of two class rooms and one store room. Its dimension: Plinth Area : L=14m and B=5.8m 2 class rooms: L=7m and B=5.8m , Store room : L=5.8m and B=5.8m Verandah: L=14m and B=1.4m, 4 No's of windows=1.5m and H=1.5m Doors: H=2m and B=0.9m , Chowkat : (6x10x380)cm. It was informed by the School Managing Committee that benches and tables have been purchased from the Scheme. The School Managing Committee was advised to make correction on the plaque with complete details.

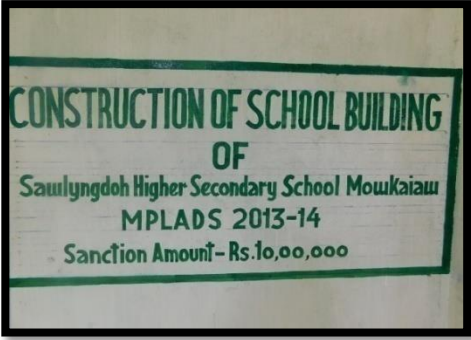


CONSTRUCTION OF BUILDING OF WOMEN GROUP & MULTIPURPOSE COOPERATIVE SOCIETY LTD. MOOKYNDENG	
  	
Date of Inspection:	26.05.2017
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G.Nongtdu, Executive Engineer and Shri L.L.Jyrwa, Junior Engineer
Accompanied by:	Shri P. Shullai, Assistant Engineer, Shri D. Chullet, Junior Engineer, Shri S. Law, Junior Engineer, Shri P. Wann, Gram Sevak and Shri M. Suchiang, Gram Sevak
Name of the Scheme:	Construction of building of Women Group & Multipurpose Cooperative Society Ltd. Mookyndeng.
Name of the MP:	Shri V.H. Pala MP(LS)
Year recommended/sanctioned:	2013-14
Amount & Date of sanctioned by the DC:	Rs 5,00,000/- sanctioned on 29 th January 2014
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1st instalment :- 2nd instalment :-	Rs. 2,50,000/- released from Block Office on 5 th June 2014. -----
Reason for delay in release of fund, if any:	Due to non submission of Utilisation Certificate to the Block Office.
Amount utilized:	Rs. 2,50,000/-
Date of commencement/starting of the work:	4 th March 2014
Date of completion/Expected date of completion:	29 th July 2014
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Nil
Name of executing agency:	The work is executed by the Local Committee
Whether signboard erected or not:	Signboard erected without the name of MP.
Date of submission of UC: 1st Instalment: 2nd Instalment:	----- -----
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	-----
Impact of the scheme:	To improve economic conditions, social status, fight poverty and unemployment.
Findings/Observations:	<ol style="list-style-type: none"> The inspection team found that the construction of a building was already completed. Its dimension : House(1) : Plinth area: B=4.55m and L=7.55m, Door: H=1.80m and Width=90cm, Chowkat (7*10*493) cm, one wooden windows (90*120). House(2) : B=5.7m and L=10m, Door: H=180cm and Width=75cm, chowkat (3No's): (5*8*455) cm, 3 windows (front side): W=70cm and H=120cm and 2 windows (back side): H=150cm and W=60cm. It was informed by the Secretary, Local Committee that the scheme has been constructed from their own expenditure and they have demanded for release of the 2nd instalment. The Secretary, Local Committee was advised to submit Utilisation Certificate and photographs of the completed scheme at the earliest. The Junior Engineer had been advised to look into the matter and brief the BDO about the problem so as to facilitate release of the 2nd instalment after the Committee had completed formalities.




CONSTRUCTION OF A NEW AND PERMANENT SCHOOLBUILDING FOR DON BOSCO R.C.L.P. SCHOOL, RALIANG	
	
Date of Inspection:	26.05.2017
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, ShriR.M.G.Nongtdu, Executive Engineer and ShriL.L.Ljyrwa, Junior Engineer
Accompanied by:	Shri P. Shullai, Assistant Engineer, Shri D. Chullet, Junior Engineer, Shri S. Law, Junior Engineer, Shri P. Wann, Gram Sevak and Shri M. Suchiang, Gram Sevak
Name of the Scheme:	Construction of a New and Permanent School Building for Don Bosco R.C.L.P. School, Raliang.
Name of the MP:	Shri V.H. Pala, MP(LS)
Year recommended/sanctioned:	2013-14
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 7 th July 2015
Reason for delay in sanction, if any:	Due to late signing of the agreement
Date of release of fund: 1st instalment :- 2nd instalment :-	Rs. 3,00,000/- released from Block Office on 11 th September 2015. Rs. 2,00,000/- released from Block Office on 26 th July 2016.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	12 th September 2015
Date of completion/Expected date of completion:	28 th July 2016
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the School Managing Committee
Whether signboard erected or not:	No
Date of submission of UC: 1st Instalment:	Submitted to the BDO, Laskein C&RD Block on 19 th May 2016.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the scheme:	Construction of School building will have positive impacts on students and community, high academic standards, teacher motivation and higher student achievements.
Findings/Observations:	<ol style="list-style-type: none"> 1. The Member, Local Committee had informed that both 1st and 2ndinstalments of MPLAD Scheme has been spent for the structural work of the building, retaining wall and slab but till now the building has not yet been completed and utilised as classroom because it is a very big hall so more funds will be needed for completion of the building. He then informed that ₹5,00,000/- has been contributed from the School Funds for the building. 2. The building consist of 4 rooms with 8 no's of columns, 6 no's Tie beams, 6 no's of floor beams. 3. Its dimension: Plinth area: L=14m and B=5.1m, Column size= (30*40)cm, Tie beam=(30*35)cm, Floor beam= (30*35)cm, Retaining wall: L=14m, B=1.9m and H=3.3m, RCC Slab: L=14m and B=6.1m, Thickness=15cm. 4. The School Managing Committee was advised to erect a plaque with complete details of the scheme.

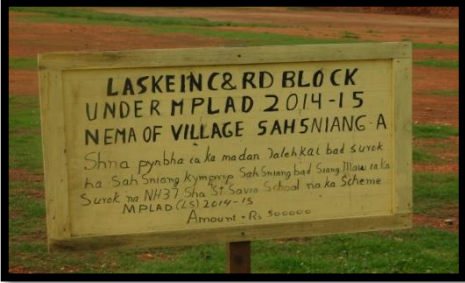


CONSTRUCTION OF COMMUNITY HALL AT SAHSNIANG SAIT THAD, SAHSNIANG






Date of Inspection:	26.05.2017
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri D. Chullet, Junior Engineer and Shri S. Law, Junior Engineer
Name of the Scheme:	Construction of Community Hall at Sahnsiang Sait thad, Sahnsiang.
Name of the MP:	Shri V.H. Pala, MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 30 th March 2016
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1st instalment :- 2nd instalment :-	Rs. 3,00,000/- released from Block Office on 14 th April 2016. Rs. 2,00,000/- released from Block Office on 19 th July 2016.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	15 th April 2016
Date of completion/Expected date of completion:	Work in progress.
Status of the work:	Work in progress.
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the local Committee.
Whether signboard erected or not:	No
Date of submission of UC: 1st Instalment: 2nd Instalment:	Submitted to the BDO, Laskein C&RD Block on 14 th June 2016. -----
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Availability of Community Hall will benefit the local people for their various needs like public awareness, Dorbar. etc.
Findings/Observations:	<ol style="list-style-type: none"> It was observed that the construction of a Community Hall is under progress. It was found that walling, casting of column, fixing of windows, chowkat, staircase are completed, whereas plastering, fixing of window glass, roofing with CGI sheet are yet to be started. The Junior Engineer was advised to do regular inspection so that the scheme will be completed on time. Its dimension: Room: L=13.6m and B=6.2m, Stage: L=6.2m and B=4.5m Verandah: L=13.6m and B=150cm, Columns (11 No's): Size=(23*23) cm, Verandah Column (5No's)=(15*15) cm and H=2.3m, Window 1(2 no's)=(90*150)cm and Window 2(2 no's)=(150*180)cm. Staircase: B=2.3m, Tread=25cm and Riser=15cm. It was informed by the Village Committee that the reason for delay in starting the construction is due to the delay in shifting of electric post by the MeECL. The Village Committee was advised to erect a plaque with complete details after completion of the scheme.

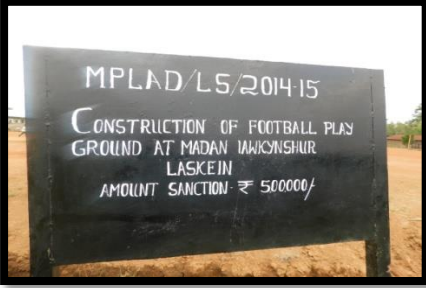


IMPROVEMENT OF PLAYGROUND AND INTERNAL ROADS AT SAHSNIANG KYMPRUP SAHSNIANG AND METALLING OF ROAD FROM NH37 TO ST. SAVIO SCHOOL.	
  	
Date of Inspection:	26.05.2017
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdo, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri D. Chullet, Junior Engineer and Shri S. Law, Junior Engineer
Name of the Scheme:	Improvement of Playground and internal roads at Sahnsiang Kymprup Sahnsiang and Metalling of road from NH37 to St. Savio School.
Name of the MP:	Shri V.H. Pala, MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 25 th August 2016
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 3,00,000/- released from Block Office on 27 th September 2016 Rs. 2,00,000/- released from Block Office on 28 th March 2017
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	29 th September 2016
Date of completion/Expected date of completion:	31 st March 2017
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the local Committee
Whether signboard erected or not:	Signboard erected but with incomplete details.
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	Submitted to the BDO Laskein C&RD Block on 31 st January 2017. -----
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	The availability of a playground will benefit the local village people who can use it for their needs like holding football tournaments, fetes, competitions, etc .
Findings/Observations:	<ol style="list-style-type: none"> 1.On inspection the team found that the Improvement of Playground and Internal Road was completed. It is observed that the filling of playground was done upto 75cm Height, repairing of existing retaining wall, earthwork cutting, laying of sub-base, base course with proper compaction. 2. Its dimension: Playground: L=100 m and B=68cm, Cutting of Earthwork: H=3m and L=60m, B=1m, Internal Road: L=500m and B=3.5m. 3. The Local Committee has been advised to erect a plaque with complete details of the scheme at the earliest.

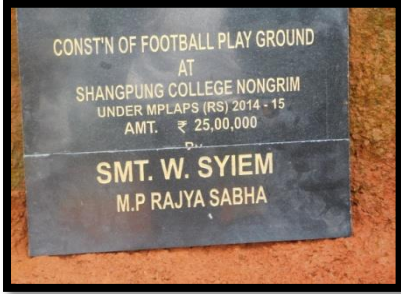CONSTRUCTION AND EXTENSION OF MADAN KHLIEHRIAT UPPER PRIMARY SCHOOL, MOOKAIAW VILLAGE	
  	
Date of Inspection:	26.05.2017
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri D. Chullet, Junior Engineer, Shri S. Law, Junior Engineer, Shri M. Suchiang, Gram Sevak and Shri B. Sutnga, Gram Sevak.
Name of the Scheme:	Construction and Extension of Madan Khliehriat Upper Primary School, Mookaiaw Village
Name of the MP:	Shri V.H. Pala, MP(LS)
Year recommended/sanctioned:	2015-16
Amount & Date of sanctioned by the DC:	Rs.10,00,000/- sanctioned on 30 th March 2016
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1st instalment :- 2nd instalment :-	Rs. 6,00,000/- released from Block Office on 14 th April 2016 Rs. 4,00,000/- released from Block Office on 19 th July 2016
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 10,00,000/-
Date of commencement/starting of the work:	15 th April 2016
Date of completion/Expected date of completion:	21 st July 2016
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the School Managing Committee
Whether signboard erected or not:	Not erected.
Date of submission of UC: 1st instalment :- 2nd instalment :-	Submitted to the BDO, Laskein C&RD Block on 9 th June 2016. -----
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Addition of extra classrooms to accommodate the students
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of school building was completed. It was constructed with good quality usage materials and workmanship. It consists of 1 classroom, 1 teacher's room, one store room and a staircase. Its dimension: Plinth area: L=15.7m and B=7.45m, Veranda: L=15.7m and B= 1.8m, Room1: L=7.75m and B=7.45m, Teacher's room cum store room: L=6.1m and B=7.45m, Column Size= (30*30)cm, Veranda Column=4no's, Tie beam=7no's (30*30) cm, Floor beam=7no's(30*30)cm Staircase: riser=20cm, tread= 30cm, stair width=165cm. Window1(3no's)=(150*150)cm, window2(1 no's)=(75*150) cm and window3(4 no's)=(240*150)cm, Doors: B=90cm and H=195cm, Chowkat=(6*10*495)cm. The School Managing Committee was advised to erect a plaque with complete details at the earliest.

CONSTRUCTION OF PLAYGROUND FOR MADAN IAWKYNSUR, LASKEIN	
<div></div>	
Date of Inspection:	26.05.2017
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri D. Chullet, Junior Engineer, Shri S. Law, Junior Engineer, Shri M. Suchiang, Gram Sevak and Shri B. Sutnga, Gram Sevak.
Name of the Scheme:	Construction of Playground for Madan Iawkynsur, Laskein
Name of the MP:	Shri V.H. Pala, MP(LS)
Year recommended/sanctioned:	2015-16
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 25 th August 2016
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 3,00,000/- released from Block Office on 13 th October 2016 Rs. 2,00,000/- released from Block Office on 14 th March 2017
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	14 th October 2016
Date of completion/Expected date of completion:	16 th March 2017
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the local Committee
Whether signboard erected or not:	Signboard erected with incomplete details.
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Laskein C&RD Block on 31 st January 2017 -----
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	The availability of a playground will benefit the School who can utilize it for their various needs like organising football tournaments, competitions, etc .
Findings/Observations	<div><div>1.</div><div>On inspection the team found that the construction of playground was completed. Earthwork cutting and filling, side slope dressing, kutcha side drains are well constructed and satisfactory.</div></div> <div><div>2.</div><div>Its dimension: L=115m and B=76m, Kutcha side drain: L=80m, B=100cm and Depth=70cm, Earthwork cutting: H=2m and L=50m.</div></div> <div><div>3.</div><div>The Local Committee has been advised to make a correction on the plaque with complete details.</div></div>

CONSTRUCTION OF FOOTBALL PLAYGROUND AT SHANGPUNG COLLEGE, NONGRIM SHANGPUNG	
  	
Date of Inspection:	26.05.2017
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdo, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri D. Chullet, Junior Engineer, Shri P. Wann, Gram Sevak and Shri M. Suchiang, Gram Sevak
Name of the Scheme:	Construction of Football Playground at Shangpung College, Nongrim Shangpung
Name of the MP:	Smt. W. Syiem, MP(RS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 25,00,000/- sanctioned on 9 th March 2015
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 15,00,000/- released from Block Office on 7 th April 2015 Rs. 10,00,000/- released from Block Office on 3 rd November 2015
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 25,00,000/-
Date of commencement/starting of the work:	8 th April 2015
Date of completion/Expected date of completion:	5 th November 2015
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the College Governing Body
Whether signboard erected or not:	Signboard erected.
Date of submission of UC: 1 st instalment :-	Submitted to the BDO, Laskein C&RD Block on 1 st September 2015
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	The availability of a playground will benefit the College who can use it for their various needs like organising football tournaments, competitions, etc .
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of football playground was completed. Earthwork cutting and filling, side slope, kutcha side drain has been executed in well manner and satisfactory. Its dimension: Playground: L=131m and B=132m, Side drain: L=7m and B=60m, Drain side: W=1.5m and H=75cm.

CONSTRUCTION OF FOOTBALL PLAYGROUND OF SHANGPUNG POHSHNONG	
	
Date of Inspection:	26.05.2017
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri P. Shullai, Assistant Engineer, Shri D. Chullet, Junior Engineer, Shri S. Law, Junior Engineer, Shri P. Wann, Gram Sevak and Shri M. Suchiang, Gram Sevak
Name of the Scheme:	Construction of Football Playground of Shangpung Pohshnong
Name of the MP:	Smt. W. Syiem, MP(RS)
Year recommended/sanctioned:	2015-16
Amount & Date of sanctioned by the DC:	Rs. 25,00,000/- sanctioned on 20 th May 2016
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1st instalment :- 2nd instalment :-	Rs. 15,00,000/- released from Block Office on 23 rd June 2016 Rs. 10,00,000/- released from Block Office on 18 th October 2016
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 25,00,000/-
Date of commencement/starting of the work:	24 th June 2016
Date of completion/Expected date of completion:	20 th October 2016
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the local Committee
Whether signboard erected or not:	No signboard erected.
Date of submission of UC: 1st instalment :-	Submitted to the BDO, Laskein C&RD Block on 28 th July 2016.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	The availability of a playground will benefit the local village people who can use it for their needs like holding football tournaments, fetes, competitions, etc.
Findings/Observations:	<ol style="list-style-type: none"> 1. On inspection the team found that the playground was an existing playground where only improvement of the work has been carried out. The work execution carried out are earthwork cutting, dressing, levelling and filling of playground upto certain height and erection of goal post. 2. Its dimension: Playground: L=100m and B= 90m, Side drain: L=75m and B= 150cm, earth cutting (right side): H=3mand L= 120m, (left side): H=3.6m and L=60m. 3. It was observed that the work executed by the executing agencies was not satisfactory as it is not commensurate with the amount sanctioned. 4. Regular supervision/inspection of the work should be undertaken to ensure quality of the work. 5. It was observed that the playground is being used as a market temporarily since the original market is under construction. 6. The Assistant Engineer has been advised to inform the Secretary, Local Committee to erect a plaque with complete details. 7 It was observed that after scrutiny of the inspection format submitted from the office of the BDO, the work was completed on 31.10.2016 whereas from the Monthly Progress Report as on 31.10.2016, vide letter No.DEV/MPR/MP(RS)/2014/1/330, dt. 10.11.16 received from the office of DC, West Jaintia Hills District, the work is still in progress.

CONSTRUCTION OF FOOTBALL PLAYGROUND AT KHLIEHRANGNAH SHANGPUNG, WEST JAINTIA HILLS	
  	
Date of Inspection:	26.05.2017
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri P. Shullai, Assistant Engineer, Shri D. Chullet, Junior Engineer, Shri S. Law, Junior Engineer, Shri P. Wann, Gram Sevak and Shri M. Suchiang, Gram Sevak
Name of the Scheme:	Construction of Football Playground at Khliehrangnah Shangpung, West Jaintia Hills
Name of the MP:	Smt. W. Syiem, MP(RS)
Year recommended/sanctioned:	2015-16
Amount & Date of sanctioned by the DC:	Rs. 25,00,000/- sanctioned on 10 th December 2015
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 15,00,000/- released from Block Office on 21 st January 2016. Rs. 10,00,000/- released from Block Office on 22 nd March 2016.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 25,00,000/-
Date of commencement/starting of the work:	22 nd January 2016
Date of completion/Expected date of completion:	25 th March 2016
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the local Committee
Whether signboard erected or not:	Signboard erected with incomplete details.
Date of submission of UC: 1 st instalment :-	Submitted to the BDO, LaskeinC&RD Block on 23 rd February 2016.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	The availability of a playground will benefit the local village people who can use it for their needs like holding football tournaments, other competitions, etc .
Findings/Observations:	1.The inspection team found that the construction of football playground is completed. The works carried out are site clearance, earthwork cutting, side slope dressing, earthwork filling which has been well executed and satisfactory. 2.Its dimension: Playground: L=115m, B=81m and H=9m, Approach Kutcha road: L=192m and W=6m. 3. It was inform by the Headman that ₹4,40,000/- had been contributed by the people of the Local Village for purchasing of land and also informed that the approach road has been constructed from the scheme. 4.The Local Committee was advised to make a correction on a plague mentioning the name of MP.
