


FINANCIAL ASSISTANCE FOR ROOM EXTENSION TO THE MULTIPURPOSE COMMUNITY HALL AT ST. GEORGE SCHOOL, SAMANDA



Date of Inspection:	29 th November 2017.
Team of inspection officers:	Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri S. Sangma, Junior Engineer, Samanda C&RD Block
Name of the Scheme:	Financial Assistance for Room Extension to the Multipurpose Community Hall at St. George School, Samanda
Name of the MP:	Smt Wansuk Syiem, MP(RS)
Year recommended/sanctioned:	2015-16
Amount & Date of sanctioned by the DC:	Rs. 10,70,550/-
Reason for delay in sanction, if any:	Nil
Date of release of fund:	
1 st instalment :-	Rs. 6,42,330/- released from Block Office on 9 th September 2015.
2 nd instalment :-	Rs. 2,67,638/- released from Block Office on -----.
3 rd instalment :-	Rs. 1,60,582/- released from Block Office on -----.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 10,70,550/-
Date of commencement/starting of the work:	18 th September 2015.
Date of completion/Expected date of completion:	2 nd November 2016.
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Head Master of St. George School, Samanda.
Whether signboard erected or not:	No
Date of submission of UC:	
1 st Instalment:	Submitted to BDO, Samanda C&RD Block on 11 th February 2016.
2 nd Instalment:	Submitted to BDO, Samanda C&RD Block on 12 th September 2016.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Multi-facility building has immensely helped to conduct meeting and other functions within the Samanda area.
Findings/Observations:	<ol style="list-style-type: none"> During inspection the team found that the room extension to the Multipurpose Community Hall at St. George School is completed. It is constructed with good quality materials. The hall consist stage, sitting gallery and it is covered with CGI sheet, plywood ceiling and with 9 (nine nos) ceiling fans. Its dimension: Plinth area of Hall: L=78m and B=9.10m-----Window (16 nos): (90cm*150cm). Gallery: Thread= 40cm and Riser: 25cm-----Gate: (200cm*200cm). Column size: (30*30) cm. The School Managing Committee has been advised to erect a plaque with a full complete details of the scheme, which include the name of the MP, year and date of sanctioned, amount sanctioned,. etc.

CONSTRUCTION OF COMMUNITY HALL AT TERRACEGITTIM



Date of Inspection:	29 th November 2017
Team of inspection officers:	Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri S. Sangma, Junior Engineer, Samanda C&RD Block
Name of the Scheme:	Construction of Community Hall at Terracegittim
Name of the MP:	Shri P.A. Sangma, MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 3,00,000/- sanctioned on -----
Reason for delay in sanction, if any:	Nil
Date of release of fund:	
1 st instalment :-	Rs. 1,80,000/- released from Block Office on 30 th March 2015.
2 nd instalment :-	Rs. 75,000/- released from Block Office on 3 rd March 2016.
3 rd instalment :-	Rs. 45,000/- released from Block Office on 17 th September 2016.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 3,00,000/-
Date of commencement/starting of the work:	May 2015.
Date of completion/Expected date of completion:	July 2016.
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	The work is executed by the Village Development Council, Terracegittim.
Whether signboard erected or not:	Yes
Date of submission of UC:	
1 st Instalment:	Submitted to BDO, Samanda C&RD Block on 11 th February 2016.
2 nd Instalment:	Submitted to BDO, Samanda C&RD Block on 25 th April 2016.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Community Hall is generally used by villagers to hold meeting and other functions.
Findings/Observations:	<ol style="list-style-type: none"> During inspection the team found that the construction of Community Hall is completed. It is constructed with good quality materials. Its dimension: Plinth area: L=8.20m and B=5.10m-----Plinth height: 80cm. Column size: (18cm *18cm) ----- Windows (2nos): (100cm*120cm) Door: (90cm*190cm).-----chowkat: (10*7 *405)cm. The Junior Engineer has been advised to inform the Committee to make correction on signboard mentioning the name of the MP, year and date of sanctioned, amount sanctioned,, etc.


Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G. Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L. Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-

FINANCIAL ASSISTANCE FOR EXTENSION OF RCC (2ND FLOOR) SCHOOL BUILDING SACRED HEART HIGHER SECONDARY SCHOOL, WILLIAMNAGAR



Date of Inspection:	29 th November 2017.	
Team of inspection officers:	Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
Accompanied by:	Shri Hitesh Medhi, Addl. Programme Officer, DRDA Williamnagar and Junior Engineer, Municipal Board.	
Name of the Scheme:	Financial Assistance for Extension of RCC (2 nd floor) School Building Sacred Heart Higher Secondary School, Williamnagar	
Name of the MP:	Smt Wansuk Syiem, MP(RS)	
Year recommended/sanctioned:	2015-16	
Amount & Date of sanctioned by the DC:	Rs. 10,78,500/- sanctioned on 11 th January 2016.	
Reason for delay in sanction, if any:	Nil	
Date of release of fund:		
1 st instalment :-	Rs. 6,47,100/- released from Block Office on 23 rd June 2015.	
2 nd instalment :-	Rs. 2,69,625/- released from Block Office on 25 th May 2016.	
3 rd instalment :-	Rs. 1,61,775/- released from Block Office on 29 th March 2017.	
Reason for delay in release of fund, if any:	Nil	
Amount utilized:	Rs. 10,78,500/-	
Date of commencement/starting of the work:	26 th June 2015.	
Date of completion/Expected date of completion:	10 th May 2017.	
Status of the work:	Completed	
Cause/Reason for delay in sanction/completion of works:	Nil	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Williamnagar Municipal Board.	
Name of executing agency:	The work is executed by the Sacred Heart Higher Secondary School, Williamnagar	
Whether signboard erected or not:	No	
Date of submission of UC:		
1 st Instalment:	Submitted to CEO, Williamnagar Municipal Board on 31 st March 2016.	
2 nd Instalment:	Submitted to CEO, Williamnagar Municipal Board on 20 th January 2017.	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	No	
Impact of the Scheme:	Accommodation of students for better education.	
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the Extension of the school building is completed the school building consist of 2 (two) classrooms. It is constructed with good quality materials and good workmanship. Its dimension: Rooms (2nos): L=9m and B=6m-----Column size: (25cm*40cm). Floor beam: (20cm*35cm)-----Windows (5 nos): (160cm *120cm). Door: (95cm*200cm)-----chowkat: (10*7 *505) cm. The School Managing Committee has been advised to erect a signboard with full complete details of the scheme, which include the name of the MP, year and date of sanctioned, amount sanctioned,. etc. 	

CONSTRUCTION OF MOTORABLE ROAD WITH INTER LOCKING: CC BLOCKS AT BALSRI RESERVE GITTIM LANE

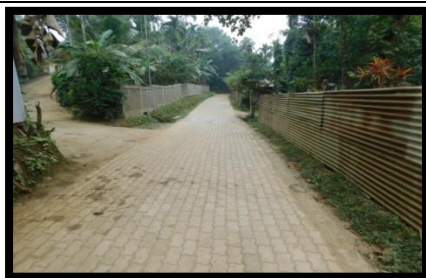

Date of Inspection:	29 th November 2017.	
Team of inspection officers:	Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
Accompanied by:	Shri Hitesh Medhi, Addl. Programme Officer, DRDA Williamnagar and Junior Engineer, Municipal Board.	
Name of the Scheme:	Construction of Motorable road with Inter Locking: CC Blocks at Balsri Reserve Gittim Lane.	
Name of the MP:	Shri Conrad K. Sangma, MP(LS)	
Year recommended/sanctioned:	2016-17	
Amount & Date of sanctioned by the DC:	Rs. 20,00,000/- sanctioned on 5 th February 2017.	
Reason for delay in sanction, if any:	Nil	
Date of release of fund: 1 st instalment :- 2 nd instalment :- 3 rd instalment :-	Rs. 12,00,000/- released from Block Office on 15 th February 2017. Rs. 5,00,000/- released from Block Office on 5 th September 2017. -----	
Reason for delay in release of fund, if any:	Nil	
Amount utilized:	Rs. 17,00,000/-	
Date of commencement/starting of the work:	17 th February 2017.	
Date of completion/Expected date of completion:	January 2018.	
Status of the work:	70% Work in progress	
Cause/Reason for delay in sanction/completion of works:	Nil	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Williamnagar Municipal Board	
Name of executing agency:	The work is executed by the Construction & Monitoring Committee	
Whether signboard erected or not:	No	
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	Submitted to CEO, Williamnagar Municipal Board on 27 th July 2017. -----	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	No	
Impact of the Scheme:	Providing access to the people of the locality.	
Findings/Observations:	<ol style="list-style-type: none"> The inspection team found that the construction of inter locking Motorable road is under progress. It was observed that the laying of interlocking block is complete upto a length of 280m and remaining length of 55m is yet to be executed. Its dimension: Length= 335m and Width= 3.30m Inter locking block size: (20*10*19.15) cm. The Secretary, Village Committee has been advised for submission of photograph and Utilisation Certificate to the BDO so that the remaining balance will be released soon. The Junior Engineer has been advised to inform the Construction & Monitoring Committee to erect a signboard on completion of the scheme. 	
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation		-
Shri R.M.G. Nongtdu, Executive Engineer, S.P.I.C, MPLADS under PI & E		-
Shri L.L.L. Jyrwa, Junior Engineer, S.P.I.C, MPLADS under PI & E		-
