

CONSTRUCTION OF FOOTBALL FENCING AT MYNSNGAT VILLAGE



Date of Inspection:	9 th June 2017	
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
Accompanied by:	Shri T. Dhar, Assistant Engineer, Shri B. Nongtdu, Gram Sevak, Shri S. Challam, Gram Sevak and Shri K. Hinge, Gram Sevak	
Name of the Scheme:	Construction of Football Fencing at Mynsngat Village.	
Name of the MP:	Smt. W. Syiem, MP(RS)	
Year recommended/sanctioned:	2015-16	
Amount & Date of sanctioned by the DC:	Rs. 5,00,900/- sanctioned on 28 th August 2016	
Reason for delay of sanction, if any:	Nil	
Date of release of fund:		
1st instalment :-	Rs. 3,00,540/- released from Block Office on 26 th September 2016.	
2nd instalment :-	Rs. 2,00,360/- released from Block Office on 26 th April 2017.	
Reason for delay in release of fund, if	Nil	
Amount utilized:	Rs. 5,00,900/-	
Date of commencement/starting of the work:	30 th September 2016	
Date of completion/Expected date of completion:	27 th April 2017	
Status of the work:	Completed	
Cause/Reason for delay in sanction/completion of works:	Nil	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.	
Name of executing agency:	The work is executed by Mynsngat Village Executive Committee.	
Whether signboard erected or not:	No.	
Date of submission of UC:		
1st Instalment:	Submitted to BDO, Thadlaskein C&RD Block on 26 th September 2016.	
2nd Instalment:	Submitted to BDO, Thadlaskein C& RD Block on 26 th April 2017.	
In case of completed Scheme whether the completion Report/ Certificate submitted to BDO/DC:	Yes	
Impact of the scheme:	Benefits in boundary demarcation, enhances good appearances of the facilities, prevents straying and hazard to road users, prevents access of vehicles, etc.	
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of football fencing is completed. The work has been executed better than the estimate and drawing plan. It is constructed with a usage of good quality materials and good workmanship. Its dimension: <ul style="list-style-type: none"> Total length of fencing- 207 Meters. No's of GI pipe- 207 no's. Length of GI pipe- 3m. Diameter of GI pipe- 200mm. Column Size (47 nos)- (25*25) cm, H-150cm. The Assistant Engineer has been advised to inform the Local Committee to erect a plaque with complete details. 	

CONSTRUCTION OF COMMUNITY HALL AT NONGTHYMMEI, SEHLAMA



Date of Inspection:	9 th June 2017	
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer	
Accompanied by:	Shri T. Dhar, Assistant Engineer, Shri B. Nongtdu, Gram Sevak, Shri S. Challam, Gram Sevak and Shri K. Hinge, Gram Sevak	
Name of the Scheme:	Construction of Community Hall at Nongthymmei, Sehlama.	
Name of the MP:	Shri V.H.Pala, MP(LS)	
Year recommended/sanctioned:	2015-16	
Amount & Date of sanctioned by the DC:	Rs 5,00,000/- sanctioned on 12 th February 2016	
Reason for delay in sanction, if any:	Nil	
Date of release of fund:		
1st instalment :-	Rs. 3,00,000/- released from Block Office on 19 th February 2016.	
2nd instalment :-	Rs. 2,00,000/- released from Block Office on 24 th June 2016.	
Reason for delay in release of fund, if any:	Nil	
Amount utilized:	Rs. 5,00,000/-	
Date of commencement/starting of the work:	20 th February 2016	
Date of completion/Expected date of completion:	-----	
Status of the work:	Work is under progress.	
Cause/Reason for delay in sanction/completion of works:	Nil	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.	
Name of executing agency:	The work is executed by the Sehlama Executive Committee.	
Whether signboard erected or not:	No.	
Date of submission of UC:		
1st Instalment:	Submitted to BDO, Thadlaskein C&RD Block on 19 th February 2016.	
2nd Instalment:	Submitted to BDO, Thadlaskein C& RD Block on 24 th June 2016.	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes	
Impact of the scheme:	Benefits the villagers to arrange group activities, social support, public information and many other purposes that will enrich the lives of the people.	
Findings/Observations:	<ol style="list-style-type: none"> 1. On inspection the team found that the construction of Community Hall is under progress. The work has been executed more than the estimate and Drawing plan. 2. It was observed that earthwork in foundation, concrete in foundation, casting of Plinth beam, casting of column is completed where as walling, flooring, and slab roofing is yet to be started. 4. Its dimension: Plinth area – L=13m and B=6.20m. Column size – (30*30) cm and H=3m. Plinth beam size – (30*30) cm. No's of Column – 10 no's and No's of Plinth beam – 13 no's. 5. It was informed by Local Committee that the work has been temporarily stopped due to rice plantation season, and the Committee has been advised to start the work as soon as possible when the plantation is over. 6. The Local Committee has been advised to erect a plaque with complete details after completion the scheme. 7. The Assistant Engineer has been advised to do regular inspection so that the work will be completed in time. 	

CONSTRUCTION OF MULANG RC UPPER PRIMARY SCHOOL, NONGBAH



Date of Inspection:	9 th June 2017	
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer	
Accompanied by:	Shri T. Dhar, Assistant Engineer, Shri B. Nongtdu, Gram Sevak, Shri S. Challam, Gram Sevak and Shri K. Hinge, Gram Sevak	
Name of the Scheme:	Construction of Mulang RC Upper Primary School, Nongbah	
Name of the MP:	Shri V.H. Pala, MP(LS)	
Year recommended/sanctioned:	2014-15	
Amount & Date of sanctioned by the DC:	Rs. 10,00,000/- sanctioned on 8 th September 2015.	
Reason for delay in sanction, if any:	Nil	
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 6,00,000/- released from Block Office on 23 rd September 2015. -----	
Reason for delay in release of fund, if any:	Non-availability of land in time.	
Amount utilized:	Rs. 6,00,000/-	
Date of commencement/starting of the work:	23 rd September 2016.	
Date of completion/Expected date of completion:	23 rd September 2017.	
Status of the work:	Work in Progress.	
Cause/Reason for delay in sanction/completion of works:	Non-availability of land.	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.	
Name of executing agency:	School Managing Committee of Mulang RC Upper Primary, Nongbah.	
Whether signboard erected or not:	No.	
Date of submission of UC: 1 st Instalment:	Submitted to the BDO, Thadlaskein C&RD Block on 23rd September 2015.	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Work in progress.	
Impact of the scheme:	Improve in literacy and education of the village children.	
Findings/Observations:	<ol style="list-style-type: none"> 1. On inspection the team found that the structural work of school building is under progress. The Team found that the work has been executed more than estimate and Drawing plan. 2. The team found that the concrete in foundation have been completed whereas casting of Plinth beams and columns, form work of beams and columns is yet to be started. 3. It was informed that the reason of delay in completion of work is due to site selection and also the work is temporarily halted due to rice plantation the Committee has been advised to start the work as soon as possible when the plantation is over. 4. It was informed by School Managing Committee that additional fund will be funded from other sources for completion of the scheme. 5. The School Managing Committee has been advised to erect a plaque with a complete details after completion the schemes. 6. The AE and GS has been advised to do regular inspection so that the work will be completed in time. 	

CONSTRUCTION OF COMMUNITY HALL AT NONGBAH VILLAGE



Date of Inspection:		9 th June 2017
Team of inspection officers:		Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:		Shri T. Dhar, Assistant Engineer, Shri B. Nongtdu, Gram Sevak, Shri S. Challam, Gram Sevak and Shri K. Hinge, Gram Sevak
Name of the Scheme:		Construction of Community Hall at Nongbah Village
Name of the MP:		Shri V.H Pala, MP(LS)
Year recommended/sanctioned:		2014-15
Amount & Date of sanctioned by the DC:		Rs. 10,00,000/- sanctioned on 8 th September 2016.
Reason for delay in sanction, if any:		Nil
Date of release of fund:		
1st instalment :-		Rs. 6,00,000/- released from Block Office on 23 rd September 2015.
2nd instalment :-		-----
Reason for delay in release of fund, if any:		Shortage of Labour.
Amount utilized:		Rs. 6,00,000/-
Date of commencement/starting of the work:		24 th September 2016.
Date of completion/Expected date of completion:		December 2017.
Status of the work:		Work in progress.
Cause/Reason for delay in sanction/completion of works:		Shortage of Labour.
Whether inspection carried out from Block/DCs office:		Yes, at regular intervals from Block Office.
Name of executing agency:		Village Headman of Nongbah village.
Whether signboard erected or not:		
Date of submission of UC:		
1st Instalment:		Submitted to the BDO, Thadlaskein C&RD Block on 23 rd September 2015.
2nd Instalment:		-----
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:		-----
Impact of the Scheme:	Benefits the villagers to arrange group activities, social support, public information and many other purposes that will with enrich the lives of people.	
Findings/Observations:	<ol style="list-style-type: none"> 1. On inspection the team found that the construction of Community hall is under progress. It is constructed with usage of good quality materials. 2. The Team found that the work has been executed not as per estimate and drawing plan. Executing of column and beam layout is not as per drawing plan. The construction involves a bigger estimate as it is a onetime investment with funds contributed from the Local Committee. 3. The team found that the concrete in foundation, columns, plinth beams and RCC Retaining wall are completed, whereas brick walling and Shuttering of beams is under progress. 4. Its dimension: Plinth area – L=22m and B=11m. Column Size – (25*25) cm, plinth beam Size – (25*25) cm. RCC Retaining wall–L=18m, H=5m and Thickness=35cm. 5. It was informed that Rs. 4 Lakhs had been contributed by the Local Committee. 6. It was informed by the Committee that they are going for release of 2nd instalment. 7. The Committee has been advised to submit Photographs and UC's to the Office of BDO in order to release the 2nd instalment. 8. The Local Committee has been advised to erect a plaque with complete details after completion of the scheme. 	

CONSTRUCTION OF FENCING FOR MOOSALYNGKAT DORBAR SHNONG, JOWAI




Date of Inspection:	9 th June 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri T. Dhar, Assistant Engineer, Shri B. Nongtdu, Gram Sevak, Shri S. Challam, Gram Sevak and Shri K. Hinge, Gram Sevak
Name of the Scheme:	Construction of Fencing for Moosalynghat Dorbar Shnong, Jowai.
Name of the MP:	Smt. W. Syiem, MP (RS).
Year recommended/sanctioned:	2015-16
Amount & Date of sanctioned by the DC:	Rs. 5,00,000/- sanctioned on 12 th February 2016.
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 3,00,000/- released from Block Office on 19 th February 2016. Rs. 2,00,000/- released from Block Office on 17 th April 2017.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 5,00,000/-
Date of commencement/starting of the work:	20 th February 2016
Date of completion/Expected date of completion:	October 2017.
Status of the work:	Work in Progress.
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	Moosalynghat Executive Committee.
Whether signboard erected or not:	No.
Date of submission of UC: 1 st Instalment: 2 nd Instalment:	Submitted to the BDO Thadlaskein C&RD Block on 19 th February 2016. Submitted to the BDO Thadlaskein C&RD Block on 17 th April 2017.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	----
Impact of the Scheme:	Boundary demarcation prevents access of intruders etc.
Findings/Observations:	<ol style="list-style-type: none"> 1. On inspection the team found that the fencing is under progress. It is constructed with usage of good quality materials. 2. Its dimension: L=30m, H=2.3m and Width=0.6cm. 3. The Assistant Engineer has been advised to inform the Local Committee to complete the work and to erect the plaque with complete details after completion of the scheme.

IMPROVEMENT OF THOMAS JONES SYNOD COLLEGE LIBRARY, JOWAI, WEST JAINTIA HILLS DISTRICT



Date of Inspection:	9 th June 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri T. Dhar, Assistant Engineer, Shri B. Nongtdu, Gram Sevak, Shri S. Challam, Gram Sevak and Shri K. Hinge, Gram Sevak
Name of the Scheme:	Improvement of Thomas Jones Synod College Library, Jowai, West Jaintia District.
Name of the MP:	Shri V.H Pala, MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs.10,00,000/- sanctioned on 12 th February 2016.
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 6,00,000/- released from Block Office on 15 th June 2016. Rs. 4,00,000/- released from Block Office on 14 th October 2016.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 10,00,000/-
Date of commencement/starting of the work:	18 th June 2016.
Date of completion/Expected date of completion:	20 th October 2016.
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	Principal of Thomas Jones Synod College, Jowai.
Whether signboard erected or not:	No.
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Thadlaskein C&RD Block on 15 th June 2016. Submitted to the BDO, Thadlaskein C&RD Block on 14 th October 2016.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Increase the interests of the student and their knowledge.
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the improvement of library at Thomas Jones Synod College is completed and well equipped with modern books, materials. The College Managing Committee had informed the inspection team that they had purchased Desktop Computers (14 Nos), UPS (14 Nos), Xerox Machine (1 No), Library Stack Double Faced (24 Nos), Installation Charge (24 Nos), Chairs (40 Nos), Elib + OPAC System (1 No), Tvs Bar Code Reader (101 stan) (1 No), Tvs Bar Code Printer (LP45) (1 No), Thermal film (1 No), Barcode sticker (2 Nos) and Books (1162 Nos). The College Managing Committee has been advised to erect a plaque with complete details of the scheme.

CONSTRUCTION OF NEW SCHOOL BUILDING FOR MARIAN HILL HIGHER SEC. SCHOOL, JOWAI

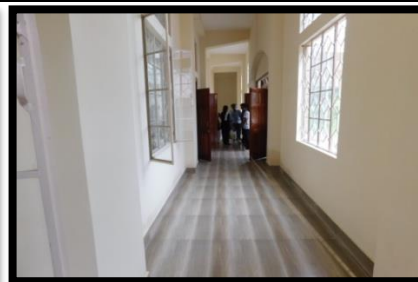

Date of Inspection:	9 th June 2017	
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer	
Accompanied by:	Shri T. Dhar, Assistant Engineer, Shri B. Nongtdu, Gram Sevak, Shri S. Challam, Gram Sevak and Shri K. Hinge, Gram Sevak	
Name of the Scheme:	Construction of New School Building for Marian Hill Higher Sec. School, Jowai.	
Name of the MP:	Shri V.H.Pala, MP(LS)	
Year recommended/sanctioned:	2013-14	
Amount & Date of sanctioned by the DC:	Rs. 30,00,000/- sanctioned on 8 th January 2014.	
Reason for delay in sanction, if any:	Nil	
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 15,00,000/- released from Block Office on 10 th July 2014. Rs. 15,00,000/- released from Block Office on 16 th July 2015.	
Reason for delay in release of fund, if any:	Nil	
Amount utilized:	Rs. 30,00,000/-	
Date of commencement/starting of the work:	15 th July 2014.	
Date of completion/Expected date of completion:	17 th July 2015.	
Status of the work:	Completed	
Cause/Reason for delay in sanction/completion of works:	Nil	
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.	
Name of executing agency:	Principal of the School (Marian Hill School)	
Whether signboard erected or not:	No.	
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Thadlaskein C&RD Block on 10 th July 2014. Submitted to the BDO, Thadlaskein C&RD Block on 16 th July 2015.	
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes	
Impact of the Scheme:	Impart Higher education to the students of Jowai town and its adjacent Villages	
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of school building is completed. It is constructed with a usage of good quality materials and good workmanship. The Team found that the work has been executed not as per estimate and drawing plan .It is beyond the Plan & Estimate as funds have been spent from the School too. Its dimension: Plinth area – L=28m and B=12m. Door (4 no's) – 120*270 cm. Window (7 no's) – 150*150 cm. Corridor – L=28m and B=1.5m. It was informed that ₹.1 Crore has been contributed by the Committee for completion of the scheme. The School Committee has been advised to erect a plaque with complete details. 	

CONSTRUCTION OF AITNAR ANNUAL CULTURAL FESTIVAL (BEHDEINKHLAM) AT MAYA CLUB WAHIAJER VILLAGE



Date of Inspection:	9 th June 2017
Team of inspection officers:	Shri E.B. Lyngdoh, Assistant Director, Shri S. Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L. Jyrwa, Junior Engineer
Accompanied by:	Shri T. Dhar, Assistant Engineer, Shri B. Nongtdu, Gram Sevak, Shri S. Challam, Gram Sevak and Shri K. Hinge, Gram Sevak
Name of the Scheme:	Construction of Aitnar Annual Cultural Festival (Behdeinkhlam) at Maya Club Wahiajer Village.
Name of the MP:	Smt. W. Syiem, MP(RS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 20,00,000/- sanctioned on 10 th December 2014.
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 10,00,000/- released from Block Office on 22 nd December 2014. Rs. 10,00,000/- released from Block Office on 12 th February 2015.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 20,00,000/-
Date of commencement/starting of the work:	26 th December 2014.
Date of completion/Expected date of completion:	10 th February 2015.
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	Wahiajer Executive (members) Committee.
Whether signboard erected or not:	No.
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Thadlaskein C&RD Block on 22 nd December 2014. Submitted to the BDO, Thadlaskein C&RD Block on 12 th February 2015.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Benefit for people in arranging various Cultural & religious events.
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of Aitnar Annual Cultural festival is completed. It is constructed with usage of good quality materials and good workmanship. The Team found that the work has been executed not as per estimate and drawing plan and is bigger and costlier. Its dimension: <ul style="list-style-type: none"> Cement Concrete Road – L=88m, Width=2.3m. Area of ground – L=88m and B=26m. Brick fencing wall – L=220m. Height of fencing wall – 1.5m. Gate – L=4m and H=2m. The Club has been advised to erect a plaque with complete details.

CONSTRUCTION OF FENCING WITH ORNAMENTAL GRILL ETC. AT MAYA CLUB, WAHIAJER VILLAGE CLUB



Date of Inspection:	9 th June 2017
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri T. Dhar, Assistant Engineer, Shri B. Nongtdu, Gram Sevak, Shri S. Challam, Gram Sevak and Shri K. Hinge, Gram Sevak
Name of the Scheme:	Construction of Fencing with Ornamental Grill Etc. at Maya Club, Wahiajer Village Club.
Name of the MP:	Smt. W. Syiem, MP(RS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 20,00,000/- sanctioned on 12 th February 2015.
Reason for delay in sanction, if any:	Nil
Date of release of fund:	
1st instalment :-	Rs. 12,00,000/- released from Block Office on 27 th February 2015.
2nd instalment :-	Rs. 8,00,000/- released from Block Office on 8 th June 2015
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 20,00,000/-
Date of commencement/starting of the work:	30 th February 2015.
Date of completion/Expected date of completion:	25 th June 2015.
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	Wahiajer Executive (members) Committee.
Whether signboard erected or not:	No.
Date of submission of UC:	
1st instalment :-	Submitted to the BDO, Thadlaskein C&RD Block on 27 th February 2015.
	Submitted to the BDO, Thadlaskein C&RD Block on 8 th June 2015.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Boundary demarcation prevents access of intruders etc.
Findings/Observations:	<p>1. On inspection the team found that the construction of fencing with ornamental is completed. It is constructed with a good usage and good quality materials and good workmanship. The Team found that the work has been executed more than estimate and drawing plan.</p> <p>2. Its dimension: Brick walling fencing – L=143m (approx) and H=1.5m. Gate1 – L=3m and H=2m. Gate2 – L=1.3m and H=1.6m. Ornamental grill – L=60m and H=1m.</p> <p>3. The Club has been advised to erect a plaque with complete details of the scheme.</p>

CONSTRUCTION OF LITTLE FLOWER HIGHER SECONDARY SCHOOL, UMMULONG



Date of Inspection:	9 th June 2017
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdo, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri T. Dhar, Assistant Engineer, Shri B. Nongtdo, Gram Sevak, Shri S. Challam, Gram Sevak and Shri K. Hinge, Gram Sevak
Name of the Scheme:	Construction of Little Flower Higher Secondary School, Ummulong.
Name of the MP:	Shri. V.H. Pala, MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 10,00,000/- sanctioned on 12 th February 2016.
Reason for delay in sanction, if any:	Nil
Date of release of fund: 1 st instalment :- 2 nd instalment :-	Rs. 6,00,000/- released from Block Office on 19 th February 2016. Rs. 4,00,000/- released from Block Office on 4 th October 2016.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 10,00,000/-
Date of commencement/starting of the work:	22 nd February 2016.
Date of completion/Expected date of completion:	8 th October 2016.
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	Principal of the School.
Whether signboard erected or not:	No.
Date of submission of UC: 1 st instalment :- 2 nd instalment :-	Submitted to the BDO, Thadlaskein C&RD Block on 19 th February 2016. Submitted to the BDO, Thadlaskein C&RD Block on 4 th October 2016.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Impact Higher Education for the Children of Ummulong Village and its neighbour's villages.
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of school building is completed. It is constructed with a good usage of good quality materials and good workmanship. The Team found that the work has been executed more than the estimate and drawing plan. <ol style="list-style-type: none"> Its dimension: It consists of 4 classrooms. Plinth area – L=26m and B=7m. Veranda – L=26m and B=2m. Windows (12 no's) – (1.5*1.2) m. Doors (4 no's) – (90*200) cm. Chowkat – (10*10*490) cm. Veranda Brick Walling – L=28m and H=1.2m. It was informed that ₹.1 Lakh has been contributed by School Managing Committee The College Managing Committee has been advised to erect a plaque with complete details of scheme.

CONSTRUCTION OF BUILDING AND BUYING OF BOOKS IN LIBRARY FOR UMMULONG PRESBYTERIAN COLLEGE



Date of Inspection:	9 th June 2017
Team of inspection officers:	Shri E.B.Lyngdoh, Assistant Director, Shri S.Sungoh, Research Officer, Shri R.M.G. Nongtdu, Executive Engineer and Shri L.L.L Jyrwa, Junior Engineer
Accompanied by:	Shri T. Dhar, Assistant Engineer, Shri B. Nongtdu, Gram Sevak, Shri S. Challam, Gram Sevak and Shri K. Hinge, Gram Sevak
Name of the Scheme:	Construction of Building and Buying of Books in Library for Ummulong Presbyterian College.
Name of the MP:	Shri. V.H. Pala, MP(LS)
Year recommended/sanctioned:	2014-15
Amount & Date of sanctioned by the DC:	Rs. 10,00,000/- sanctioned on 8 th September 2015.
Reason for delay in sanction, if any:	Nil
Date of release of fund:	
1 st instalment :-	Rs. 6,00,000/- released from Block Office on 23 rd September 2015.
2 nd instalment :-	Rs. 4,00,000/- released from Block Office on 4 th November 2016.
Reason for delay in release of fund, if any:	Nil
Amount utilized:	Rs. 10,00,000/-
Date of commencement/starting of the work:	26 th September 2015.
Date of completion/Expected date of completion:	4 th November 2016.
Status of the work:	Completed
Cause/Reason for delay in sanction/completion of works:	Nil
Whether inspection carried out from Block/DCs office:	Yes, at regular intervals from Block Office.
Name of executing agency:	College Managing Committee.
Whether signboard erected or not:	Yes
Date of submission of UC:	
1 st instalment :-	Submitted to the BDO, Thadlaskein C&RD Block on 23 rd September 2015.
2 nd instalment :-	Submitted to the BDO, Thadlaskein C&RD Block on 4 th November 2016.
In case of completed scheme whether the completion Report/Certificate submitted to BDO/DC:	Yes
Impact of the Scheme:	Increase the interests of the students and their knowledge achievement.
Findings/Observations:	<ol style="list-style-type: none"> On inspection the team found that the construction of building & buying of books is Completed. It is constructed with a usage of good materials and with good workmanship. The Team found that the work has been executed more than the estimate and drawing plan. Its dimension: <ul style="list-style-type: none"> Plinth area – L=20m and B=7m. Teacher’s Common Room – L=7m and B=3m. Window (4 no’s) = (60*120) cm. Door – (75*180) cm -----Chowkat – (10*10* 435) cm. Class Room1 & Room2 – L=7m and B=3m. Windows 1 (10 no’s) – (90*120) cm. Doors 1 (2 no’s) – (90*175) cm----- Chowkat 1 – (10*10 *435) cm. Staircase dimension: <ul style="list-style-type: none"> L=6m, W=2.5m, Riser=25cm and Tread=25cm. Brick Railing – L=7m (Both sides) and H=0.9m. The College Managing Committee had informed us that they had purchased 1800 no’s of Books in the library. It was informed that ₹.1 Lakh has been contributed by the College Managing Committee.

Shri E.B. Lyngdoh, Assistant Director Programme Implementation & Evaluation	-
Shri S. Sungoh, Research Officer Programme Implementation & Evaluation	-
Shri R.M.G. Nongtdu, Executive Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
Shri L.L.L. Jyrwa, Junior Engineer State Project Implementation Cell of MPLADS under PI & Evaluation	-
