

## PMGSY INSPECTION REPORT

- 1) Date of Inspection :- 6-08-2015
- 2) Details of Location :- i) Village – Nongpyrdet  
ii) Block – Umsning  
iii) District – Ri-Bhoi
- 3) Name of the Scheme :- PMGSY.
- 4) Year of Sanctioned :- 2012-13
- 5) Amount Sanctioned :- Rs. 100.65 Lakhs
- 6) Amount Utilized till date/completion:- Rs. 30.339 Lakhs
- 7) Maintenance Cost:- Rs. 10.15 Lakhs.
- 8) Date of commencement of the work :- 2-4-2014
- 9) Target date of Completion:- October, 2015
- 10) Date of Completion :- 98% completed.
- 11) Physical progress of the work till date :- 98% completed.
- 12) Name of executing agency :- SRRDA Ri-Bhoi.
- 13) Whether there is any revised estimate :- Nil.
- 14) The Quality of construction of the road and side drain:- Good
- 15) Earth cutting of the road and construction of side drain :- Completed
- 16) The length of the motorable road connecting from B.K.D Road to Nongpyrdet village is 1.998 KM.



Hume Pipe



Side Drain of the road

17) Width of the road :- 3 metres.

18) Observations/findings:- The inspection team found that the newly constructed road has been Black Topped. The remaining work to be done is only the furniture signs.

19) Suggestions:- The AEE, i/c was advised to complete the remaining work as early as possible so that the same will be fully completed.



Sign Board of the road

Shri.D.S.Kharpan, Assistant Director,  
Programme Implementation & Evaluation

Shri. M. C.Khonglah, Research Assistant,  
Programme Implementation & Evaluation

## PMGSY INSPECTION REPORT

- 1) Date of Inspection :- 6-08-2015
- 2) Team of Inspecting Officers :- Shri D. S. Kharpan, Asstt. Director and Shri M.C. Khonglah, Research Asstt. accompanied by Shri D. Laloo, AEE, Shri I. Bairo JE
- 3) Details of Location :- i) Village – Mawthei  
ii) Block – Umsning  
iii) District – Ri-Bhoi
- 4) Name of the Scheme :- PMGSY.
- 5) Year of Sanctioned :- 2012-13
- 6) Amount Sanctioned :- Rs. 778.78 Lakhs
- 7) Amount Utilized till date/completion:- Rs.151.793 lakhs
- 8) Maintenance Cost :- Rs. 78.91 Lakhs.
- 9) Date of commencement of the work :- 18-3-2014
- 10) Target date of Completion:- September, 2015
- 11) Date of Completion :- Work in Progress (95 % Completed)
- 12) Physical progress of the work till date : 95 % Completed.
- 13) Name of executing agency :- SRRDA,Ri-Bhoi District
- 14) Whether there is any revised estimate :- Nil.
- 15) The Quality of construction of the road and side drain:- Good.
- 16) Earth cutting of the road and construction of side drain :- Good



Side Drain of the Road

17) The length of the motorable road connecting from 66 km BB road to Mawthei village is 8.6 KM.

18) Width of the road :- 3 metres.

19) Observation/findings:- The inspection team found that the construction of the road is 95% completed and Black Topping has been done. The only remaining work to be done are the furniture signs which will be carried out shortly.



Sign Board of the road

20) Suggestions:- The AEE, incharged was advised to complete the minor remaining work as early as possible so that the work will be fully completed.



## PMGSY INSPECTION REPORT

- 1) Date of Inspection :- 6-08-2015
- 2) Details of Location :- i) Village – Madan Nonglakhiat  
ii) Block – Umsning  
iii) District – Ri-Bhoi
- 3) Name of the Scheme :- PMGSY.
- 4) Year of Sanctioned :- 2012-13
- 5) Amount Sanctioned :- Rs.150.14 Lakhs
- 6) Amount Utilized till date/completion:- Rs.20.456 Lakhs
- 7) Maintenance Cost:- Rs. 15.18 Lakhs.
- 8) Date of commencement of the work :- 18-3-2014
- 9) Target date of Completion:- September, 2015
- 10) Date of Completion :- Work in progress (96% completed)
- 11) Physical progress of the work till date : 96% completed.
- 12) Name of executing agency :- SRRDA, Ri-Bhoi.
- 13) Whether there is any revised estimate :- Nil.
- 14) The Quality of construction of the road and side drain:- Good
- 15) Earth cutting of the road and construction of side drain :- Good



16) The length of the motorable road connecting from DT Road to Madan Nonglakhiat village is 3.373 KM.

17) Width of the road :- 3 metres.

18) Observations/findings:- The inspection team found that about 96% the work is completed and Black Topping has been done whereas furniture signs are yet to be done.

19) Suggestions:- The AEE, incharge was advised to complete the remaining work immediately after the end of monsoon so that the work will be fully completed.



Sign Board of the road

## PMGSY INSPECTION REPORT

- 1) Date of Inspection :- 6-08-2015
- 2) Details of Location :- i) Village – Mawlwai  
ii) Block – Umsning  
iii) District – Ri-Bhoi
- 3) Name of the Scheme :- PMGSY.
- 4) Year of Sanctioned :- 2012-13
- 5) Amount Sanctioned :- Rs. 415.27 Lakhs
- 6) Amount Utilized till date/completion:-Rs. 83.034 Lakhs
- 7) Maintenance Cost:- Rs.42.14 Lakhs.
- 8) Date of commencement of the work :- 18-3-2014
- 9) Target date of Completion:- September, 2015
- 10) Date of Completion :- Work in progress.
- 11) Physical progress of the work till date : 40 % over all completed.
- 12) Name of executing agency :- SRRDA Ri-Bhoi.
- 13) Whether there is any revised estimate :- Nil.
- 14) The Quality of construction of the road and side drain:-  
Work in progress
- 15) Earth cutting of the road and construction of side drain :-  
Earth work 90% completed.
- 16) The length of the motorable road connecting from Kyrdem to Mawlwai village is 4.80 KM.
- 17) Width of the road :- 3 metres.



Side Drain of the road

18) Observations/findings:- It was found that only earth cutting of the road has been completed. On the day of inspection it was observed that no labourers are present at the site and on enquiry about the absence of labourers the AEE incharge informed that due to monsoon the work has been temporarily stopped and the same will be resumed soon after the end of the monsoon.



Sign board of the road

19) Suggestions:- The AEE i/c was advised to restart the work immediately after the end of the monsoon so that the work could be completed in time.



## PMGSY INSPECTION REPORT


- 1) Date of Inspection :- 6-08-2015
- 2) Details of Location :- i) Village – Umtangling  
ii) Block – Umsning  
iii) District – Ri-Bhoi
- 3) Name of the Scheme :- PMGSY.
- 4) Year of Sanctioned :- 2012-13
- 5) Amount Sanctioned :- Rs. 261.08 Lakhs
- 6) Amount Utilized till date/completion:- Rs.52.934 Lakhs
- 7) Maintenance Cost:- Rs. 26.26 Lakhs.
- 8) Date of commencement of the work :- 18-3-2014
- 9) Target date of Completion:- September, 2015
- 10) Date of Completion :- Work in progress
- 11) Physical progress of the work till date : 70-75 %  
Completed
- 12) Name of executing agency :- SRRDA, Ri-Bhoi.
- 13) Whether there is any revised estimate :- Nil.
- 14) The Quality of construction of the road and side drain:-  
Good
- 15) Earth cutting of the road and construction of side drain  
:- Good
- 16) The length of the motorable road connecting from  
Nonglum to Umtangling village is 3.175 KM.



17) Width of the road :- 3 metres.

18) Observations:- The inspection team found that earth cutting and laying of gravels has been completed whereas only 60% of Black Topping has been done.

19) Suggestions:- The AEE incharge was advised to black top the remaining portion of the road immediately after the end of the monsoon so as to avoid early damage.

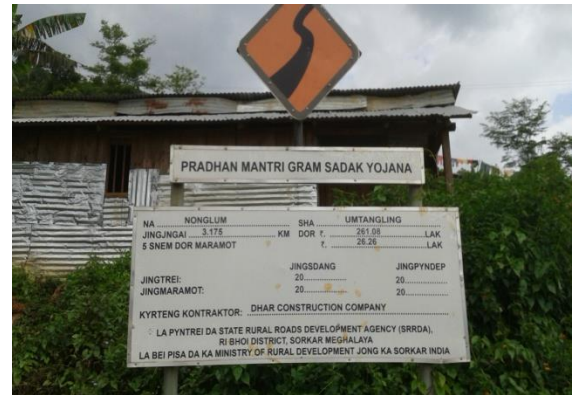

Sign Board of the road
